


Tronox Phase B Remediation Program Schedule

February 12, 2010 Preliminary Draft-in-Progress For Discussion Purposes Only


ID	Task Name	Duration	Start	Finish	Predecessor:	4th Quart	1st Quart	2nd Quart	3rd Quart	4th Quart		
						Oct	e	Jan	e	a	Apr	a
1	Phase B Investigation Program	471 days	Wed 4/15/09	Wed 2/2/11								
2	Finalize Phase B Site Investigation	447 days	Wed 4/15/09	Thu 12/30/10								
3	PM/Client/Agency Coordination	436 days	Mon 4/20/09	Mon 12/20/10								
4	Weekly Status Calls	436 days	Mon 4/20/09	Mon 12/20/10								
92	Data Mgmt/Validation	447 days	Wed 4/15/09	Thu 12/30/10								
93	Database Management	447 days	Wed 4/15/09	Thu 12/30/10								
94	Source Area I Laboratory Data Validation	25 days	Fri 10/16/09	Thu 11/19/09								
95	Source Area II Laboratory Data Validation	43 days	Wed 11/18/09	Fri 1/15/10								
96	Source Area IV Laboratory Data Validation	35 days	Wed 12/16/09	Tue 2/2/10								
97	Source Area III Laboratory Data Validation	24 days	Thu 12/31/09	Tue 2/2/10								
98	NDEP Phase B Source Area Meetings	15 days	Mon 1/18/10	Fri 2/5/10								
99	NDEP Meeting	15 days	Mon 1/18/10	Fri 2/5/10								
100	Meeting Material Preparation	14 days	Mon 1/18/10	Thu 2/4/10	95							
101	Agency Meeting	1 day	Fri 2/5/10	Fri 2/5/10	100							
102	Phase B Reporting	82 days	Fri 11/20/09	Mon 3/15/10								
103	Data Validation Summary Report - Area I	41 days	Fri 11/20/09	Fri 1/15/10								
109	Data Validation Summary Report - Area II	35 days	Mon 1/18/10	Fri 3/5/10								
110	Internal Draft DVSR	17 days	Mon 1/18/10	Tue 2/9/10	95							
111	Client Review/Draft Finalization	3 days	Wed 2/10/10	Fri 2/12/10	110							
112	Submit to NDEP	0 days	Fri 2/12/10	Fri 2/12/10	111							
113	NDEP Review	5 days	Mon 2/15/10	Fri 2/19/10	112							
114	Respond to Comments/DVSR Finalization	10 days	Mon 2/22/10	Fri 3/5/10	113							
115	Data Validation Summary Report - Area IV	28 days	Wed 2/3/10	Fri 3/12/10								
116	Internal Draft DVSR	12 days	Wed 2/3/10	Thu 2/18/10	96							
117	Client Review/Draft Finalization	1 day	Fri 2/19/10	Fri 2/19/10	116							
118	Submit to NDEP	0 days	Fri 2/19/10	Fri 2/19/10	117							
119	NDEP Review	5 days	Mon 2/22/10	Fri 2/26/10	118							
120	Respond to Comments/DVSR Finalization	10 days	Mon 3/1/10	Fri 3/12/10	119							
121	Data Validation Summary Report - Area III	28 days	Wed 2/3/10	Fri 3/12/10								
122	Internal Draft DVSR	11 days	Wed 2/3/10	Wed 2/17/10	97							
123	Client Review/Draft Finalization	2 days	Thu 2/18/10	Fri 2/19/10	122							
124	Submit to NDEP	0 days	Fri 2/19/10	Fri 2/19/10	123							
125	NDEP Review	5 days	Mon 2/22/10	Fri 2/26/10	124							
126	Respond to Comments/DVSR Finalization	10 days	Mon 3/1/10	Fri 3/12/10	125							
127	Data Validation Summary Report - Groundwater	29 days	Wed 2/3/10	Mon 3/15/10								
128	Internal Draft DVSR	12 days	Wed 2/3/10	Thu 2/18/10	97							
129	Client Review/Draft Finalization	2 days	Fri 2/19/10	Mon 2/22/10	128							
130	Submit to NDEP	0 days	Mon 2/22/10	Mon 2/22/10	129							
131	NDEP Review	5 days	Tue 2/23/10	Mon 3/1/10	130							
132	Respond to Comments/DVSR Finalization	10 days	Tue 3/2/10	Mon 3/15/10	131							
133	Remediation Planning	59 days	Mon 12/7/09	Thu 2/25/10								
134	Conceptual Remediation Planning/Prelim Risk Eval	59 days	Mon 12/7/09	Thu 2/25/10								
135	Area 1	41 days	Mon 12/7/09	Mon 2/1/10								
136	Area II	15 days	Mon 1/18/10	Fri 2/5/10	95							
137	Area IV	17 days	Wed 2/3/10	Thu 2/25/10	96							
138	Area III	17 days	Wed 2/3/10	Thu 2/25/10	97							
139	Phase B Remediation Characterization Sampling	175 days	Mon 11/23/09	Fri 7/23/10								
140	Area I	43 days	Mon 11/23/09	Wed 1/20/10								
141	Field Coordination/GBP	10 days	Mon 11/23/09	Fri 12/4/09								
142	Field Sampling	3 days	Mon 12/7/09	Wed 12/9/09	141							



Tronox Phase B Remediation Program Schedule

February 12, 2010 Preliminary Draft-in-Progress For Discussion Purposes Only

ID	Task Name	Duration	Start	Finish	Predecessor:	4th Quart		1st Quart		2nd Quart		3rd Quart		4th Quart	
						Oct	e	Jan	e	Apr	a	Jul	u	e	Oct
143	Laboratory Analysis	30 days	Thu 12/10/09	Wed 1/20/10	142										
144	Area II	49 days	Mon 12/7/09	Thu 2/11/10											
145	Field Coordination/GBP	5 days	Mon 12/7/09	Fri 12/11/09	141										
146	Field Sampling	4 days	Mon 12/14/09	Thu 12/17/09	142SS,145										
147	Laboratory Analysis	30 days	Fri 12/18/09	Thu 1/28/10	146										
148	TCLP Analysis	10 days	Fri 1/29/10	Thu 2/11/10	147										
149	Submittal of Analysis Profile to Landfills	0 days	Thu 2/11/10	Thu 2/11/10	148										
150	Acceptance of Profile Information by Landfills	10 days	Fri 2/12/10	Thu 2/25/10	149										
151	Data Validation and Summary Report	37 days	Mon 2/15/10	Tue 4/6/10											
152	Submittal of EDDs to NDEP/Neptune	0 days	Mon 2/15/10	Mon 2/15/10											
153	Data Validation	10 days	Mon 2/15/10	Fri 2/26/10	152										
154	Draft DVSR	10 days	Mon 3/1/10	Fri 3/12/10	153										
155	Client Review/Draft Finalization	2 days	Mon 3/15/10	Tue 3/16/10	154										
156	Submit to NDEP	0 days	Tue 3/16/10	Tue 3/16/10	155										
157	NDEP Review	5 days	Wed 3/17/10	Tue 3/23/10	156										
158	Respond to Comments/DVSR Finalization	10 days	Wed 3/24/10	Tue 4/6/10	157										
159	Supplemental Remediation Sampling - Site Wide	77 days	Wed 2/24/10	Thu 6/10/10											
160	Scoping	5 days	Wed 2/24/10	Tue 3/2/10	138FS-2 day										
161	Work Plan	10 days	Wed 3/3/10	Tue 3/16/10											
162	Work Plan Draft	5 days	Wed 3/3/10	Tue 3/9/10	160										
163	Tronox/Chartis Review	3 days	Wed 3/10/10	Fri 3/12/10	162										
164	Submittal to NDEP	0 days	Fri 3/12/10	Fri 3/12/10	163										
165	NDEP Approval	2 days	Mon 3/15/10	Tue 3/16/10	164										
166	Bid Development	7 days	Wed 3/17/10	Thu 3/25/10	165										
167	SOW preparation	2 days	Wed 3/17/10	Thu 3/18/10											
168	Submittal to Contractors	0 days	Thu 3/18/10	Thu 3/18/10	167										
169	Contractor Selection	5 days	Fri 3/19/10	Thu 3/25/10	168										
170	Notice to Proceed	0 days	Thu 3/25/10	Thu 3/25/10	169										
171	Field Work	15 days	Fri 3/26/10	Thu 4/15/10	170										
172	Field Coordination/GBP	10 days	Fri 3/26/10	Thu 4/8/10	165,170										
173	Field Sampling	5 days	Fri 4/9/10	Thu 4/15/10	172										
174	Laboratory Analysis	20 days	Fri 4/16/10	Thu 5/13/10	173										
175	Data Validation	20 days	Fri 5/14/10	Thu 6/10/10	174										
176	Data Validation Summary Report - Add'l Sampling	31 days	Fri 6/11/10	Fri 7/23/10											
177	Internal Draft DVSR	11 days	Fri 6/11/10	Fri 6/25/10	175										
178	Client Review/Draft Finalization	5 days	Mon 6/28/10	Fri 7/2/10	177										
179	Submit to NDEP	0 days	Fri 7/2/10	Fri 7/2/10	178										
180	NDEP Review	5 days	Mon 7/5/10	Fri 7/9/10	179										
181	Respond to Comments/DVSR Finalization	10 days	Mon 7/12/10	Fri 7/23/10	180										
182	NDEP Meeting	11 days	Fri 5/14/10	Fri 5/28/10											
183	Meeting Material Preparation	10 days	Fri 5/14/10	Thu 5/27/10	174										
184	Agency Meeting	1 day	Fri 5/28/10	Fri 5/28/10	183										
185	Tech Memos - Data Summary Reports	45 days	Fri 5/14/10	Thu 7/15/10											
186	Area I	45 days	Fri 5/14/10	Thu 7/15/10											
187	Draft Report Preparation	20 days	Fri 5/14/10	Thu 6/10/10	174										
188	Client Review/Draft Finalization	10 days	Fri 6/11/10	Thu 6/24/10	187										
189	Submit to NDEP	0 days	Thu 6/24/10	Thu 6/24/10	188										
190	NDEP Review	5 days	Fri 6/25/10	Thu 7/1/10	189										
191	Respond to Comments/Report Finalization	10 days	Fri 7/2/10	Thu 7/15/10	190										
192	Area II	45 days	Fri 5/14/10	Thu 7/15/10											

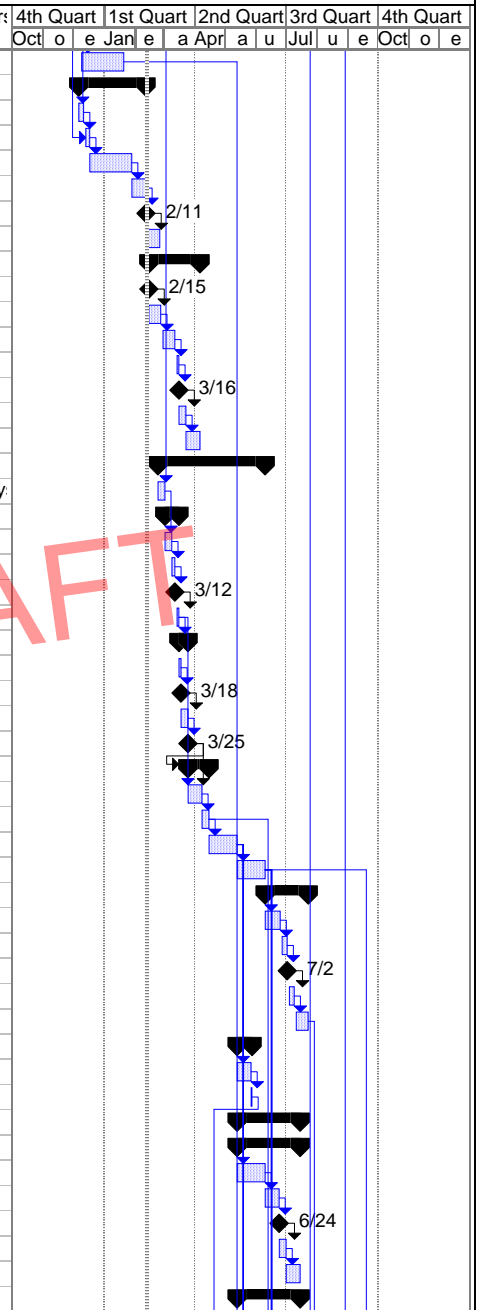


Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

Tronox Phase B Remediation Program Schedule

February 12, 2010 Preliminary Draft-in-Progress For Discussion Purposes Only

ID	Task Name	Duration	Start	Finish	Predecessor:	4th Quart	1st Quart	2nd Quart	3rd Quart	4th Quart
						Oct o	e Jan e	a Apr a	u Jul u	e Oct o
193	Draft Report Preparation	20 days	Fri 5/14/10	Thu 6/10/10	174					
194	Client Review/Draft Finalization	10 days	Fri 6/11/10	Thu 6/24/10	193					
195	Submit to NDEP	0 days	Thu 6/24/10	Thu 6/24/10	194					
196	NDEP Review	5 days	Fri 6/25/10	Thu 7/1/10	195					
197	Respond to Comments/Report Finalization	10 days	Fri 7/2/10	Thu 7/15/10	196					
198	Area IV	45 days	Fri 5/14/10	Thu 7/15/10						
199	Draft Report Preparation	20 days	Fri 5/14/10	Thu 6/10/10	174					
200	Client Review/Draft Finalization	10 days	Fri 6/11/10	Thu 6/24/10	199					
201	Submit to NDEP	0 days	Thu 6/24/10	Thu 6/24/10	200					
202	NDEP Review	5 days	Fri 6/25/10	Thu 7/1/10	201					
203	Respond to Comments/Report Finalization	10 days	Fri 7/2/10	Thu 7/15/10	202					
204	Area III	45 days	Fri 5/14/10	Thu 7/15/10						
205	Draft Report Preparation	20 days	Fri 5/14/10	Thu 6/10/10	174					
206	Client Review/Draft Finalization	10 days	Fri 6/11/10	Thu 6/24/10	205					
207	Submit to NDEP	0 days	Thu 6/24/10	Thu 6/24/10	206					
208	NDEP Review	5 days	Fri 6/25/10	Thu 7/1/10	207					
209	Respond to Comments/Report Finalization	10 days	Fri 7/2/10	Thu 7/15/10	208					
210	Corrective Action Plan (Including HASP, PAMP, SWPPP)	114 days	Mon 2/1/10	Thu 7/8/10						
211	Corrective Action Plan - Mn Tailings (PAMP only - do we need at all?)	40 days	Mon 2/1/10	Fri 3/26/10						
212	CAP Preparation	25 days	Mon 2/1/10	Fri 3/5/10						
213	Review CAP (Tronox, Chartis)	5 days	Mon 3/8/10	Fri 3/12/10	212					
214	Revise and Finalize CAP	5 days	Mon 3/15/10	Fri 3/19/10	212,213					
215	Submit CAP to NDEP	0 days	Fri 3/19/10	Fri 3/19/10	214					
216	NDEP Review and Approve CAP	5 days	Mon 3/22/10	Fri 3/26/10	215					
217	Corrective Action Plan - Area I	40 days	Mon 5/3/10	Fri 6/25/10						
218	CAP Preparation	25 days	Mon 5/3/10	Fri 6/4/10	184FS-20 da					
219	Review CAP (Tronox, Chartis)	5 days	Mon 6/7/10	Fri 6/11/10	218					
220	Revise and Finalize CAP	5 days	Mon 6/14/10	Fri 6/18/10	218,219,173					
221	Submit CAP to NDEP	0 days	Fri 6/18/10	Fri 6/18/10	220					
222	NDEP Review and Approve CAP	5 days	Mon 6/21/10	Fri 6/25/10	221					
223	Corrective Action Plan - Area II	30 days	Fri 5/14/10	Thu 6/24/10						
224	CAP Preparation	15 days	Fri 5/14/10	Thu 6/3/10	143FS-20 da					
225	Review CAP (Tronox, Chartis)	5 days	Fri 6/4/10	Thu 6/10/10	224					
226	Revise and Finalize CAP	5 days	Fri 6/11/10	Thu 6/17/10	225,224,175					
227	Submit CAP to NDEP	0 days	Thu 6/17/10	Thu 6/17/10	226					
228	NDEP Review and Approve CAP	5 days	Fri 6/18/10	Thu 6/24/10	227					
229	Corrective Action Plan - Area IV	40 days	Fri 5/14/10	Thu 7/8/10						
230	CAP Preparation	15 days	Fri 5/14/10	Thu 6/3/10	174					
231	Review CAP (Tronox, Chartis)	10 days	Fri 6/4/10	Thu 6/17/10	230					
232	Revise and Finalize CAP	10 days	Fri 6/18/10	Thu 7/1/10	231,175					
233	Submit CAP to NDEP	0 days	Thu 7/1/10	Thu 7/1/10	232					
234	NDEP Review and Approve CAP	5 days	Fri 7/2/10	Thu 7/8/10	233					
235	Corrective Action Plan - Area III	35 days	Fri 5/14/10	Thu 7/1/10						
236	CAP Preparation	10 days	Fri 5/14/10	Thu 5/27/10	174					
237	Review CAP (Tronox, Chartis)	10 days	Fri 5/28/10	Thu 6/10/10	236					
238	Revise and Finalize CAP	10 days	Fri 6/11/10	Thu 6/24/10	237					
239	Submit CAP to NDEP	0 days	Thu 6/24/10	Thu 6/24/10	238					
240	NDEP Review and Approve CAP	5 days	Fri 6/25/10	Thu 7/1/10	239					
241	Plans And Specifications/Contractor Selection	154 days	Mon 2/1/10	Thu 9/2/10						
242	Demolition	66 days	Mon 2/15/10	Mon 5/17/10						

PRELIMINARY DRAFT

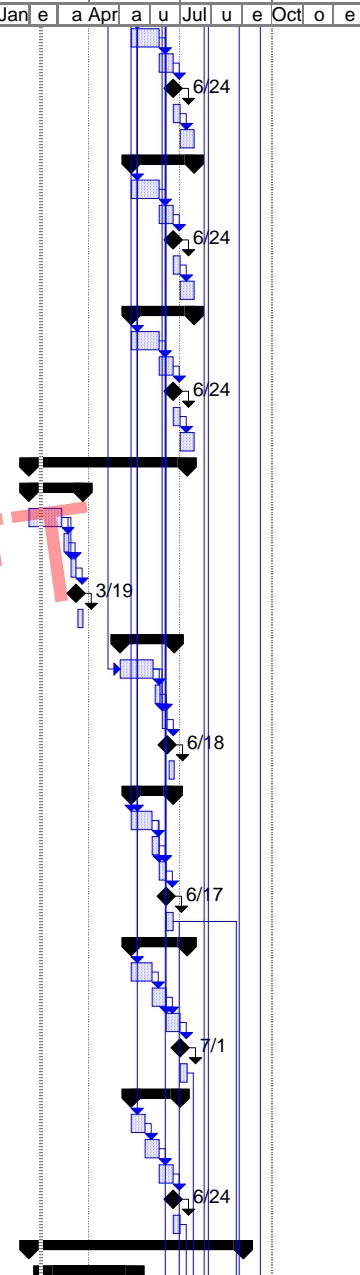


Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

Tronox Phase B Remediation Program Schedule

February 12, 2010 Preliminary Draft-in-Progress For Discussion Purposes Only

ID	Task Name	Duration	Start	Finish	Predecessor:	4th Quart 1st Quart 2nd Quart 3rd Quart 4th Quart				
						Oct	e	Jan	e	Apr
243	Regulated Building Material Surveys	35 days	Mon 2/15/10	Fri 4/2/10						
244	Bid Specifications	5 days	Mon 2/15/10	Fri 2/19/10						
245	Submit Bid Specs	0 days	Fri 2/19/10	Fri 2/19/10	244					
246	Receive Bids	5 days	Mon 2/22/10	Fri 2/26/10	245					
247	Select Contractor	5 days	Mon 3/1/10	Fri 3/5/10	246					
248	Conduct Surveys	20 days	Mon 3/8/10	Fri 4/2/10	247					
249	Prepare Remediation Plans and Specifications	35 days	Mon 3/1/10	Fri 4/16/10	248FF+10 da					
250	Review Plans and Specifications (Tronox, Chartis)	5 days	Mon 4/19/10	Fri 4/23/10	249					
251	Issue Plans and Specifications	5 days	Mon 4/26/10	Fri 4/30/10	250					
252	Bid Walk	1 day	Mon 5/3/10	Mon 5/3/10	251					
253	Bid Submittal Date	5 days	Tue 5/4/10	Mon 5/10/10	252					
254	Review Bids and Award Contract	5 days	Tue 5/11/10	Mon 5/17/10	253					
255	Remediation	154 days	Mon 2/1/10	Thu 9/2/10						
256	Site Wide - less specific detail for remediation areas	46 days	Mon 2/1/10	Mon 4/5/10						
257	Prepare Remediation Plans and Specifications	25 days	Mon 2/1/10	Fri 3/5/10						
258	Review Plans and Specifications (Tronox, Chartis)	5 days	Mon 3/8/10	Fri 3/12/10	257					
259	Issue Plans and Specifications	5 days	Mon 3/15/10	Fri 3/19/10	258					
260	Bid Walk	1 day	Mon 3/22/10	Mon 3/22/10	259					
261	Bid Submittal Date	5 days	Tue 3/23/10	Mon 3/29/10	260					
262	Review Bids and Award Contract	5 days	Tue 3/30/10	Mon 4/5/10	261					
263	Mn Tailings	20 days	Fri 2/12/10	Thu 3/11/10						
264	Prepare Remediation Plans and Specifications	10 days	Fri 2/12/10	Thu 2/25/10						
265	Review Plans and Specifications (Tronox, Chartis)	5 days	Fri 2/26/10	Thu 3/4/10	264					
266	Issue Plans and Specifications	5 days	Fri 3/5/10	Thu 3/11/10	265					
267	Area I	20 days	Mon 2/15/10	Fri 3/12/10						
268	Prepare Remediation Plans and Specifications	10 days	Mon 2/15/10	Fri 2/26/10						
269	Review Plans and Specifications (Tronox, Chartis)	5 days	Mon 3/1/10	Fri 3/5/10	268					
270	Issue Plans and Specifications	5 days	Mon 3/8/10	Fri 3/12/10	269					
271	Area II	35 days	Fri 6/25/10	Thu 8/12/10						
272	Prepare Remediation Plans and Specifications	25 days	Fri 6/25/10	Thu 7/29/10	271					
273	Review Plans and Specifications (Tronox, Chartis)	5 days	Fri 7/30/10	Thu 8/5/10	272					
274	Issue Plans and Specifications	5 days	Fri 8/6/10	Thu 8/12/10	273					
275	Area IV	40 days	Fri 7/9/10	Thu 9/2/10						
276	Prepare Remediation Plans and Specifications	30 days	Fri 7/9/10	Thu 8/19/10	275					
277	Review Plans and Specifications (Tronox, Chartis)	5 days	Fri 8/20/10	Thu 8/26/10	276					
278	Issue Plans and Specifications	5 days	Fri 8/27/10	Thu 9/2/10	277,228					
279	Area III	40 days	Fri 7/2/10	Thu 8/26/10						
280	Prepare Remediation Plans and Specifications	30 days	Fri 7/2/10	Thu 8/12/10	279					
281	Review Plans and Specifications (Tronox, Chartis)	5 days	Fri 8/13/10	Thu 8/19/10	280					
282	Issue Plans and Specifications	5 days	Fri 8/20/10	Thu 8/26/10	281					
283	Grading and Dust Monitoring Permit	139 days	Mon 2/15/10	Thu 8/26/10						
284	Permits - Mn Tailings	15 days	Mon 2/15/10	Fri 3/5/10						
285	Permits - Other Areas	15 days	Fri 8/6/10	Thu 8/26/10	274FS-5 day					
286	Contractor Submits Grading and DMP	5 days	Tue 4/6/10	Mon 4/12/10	285					
287	City of Henderson Review/Permitting	6 days	Tue 4/13/10	Tue 4/20/10	286					
288	Issue Permits	5 days	Wed 4/21/10	Tue 4/27/10	287					
289	Demolition	50 days	Tue 5/18/10	Mon 7/26/10						
290	Demolish Applicable Bldgs	30 days	Tue 5/18/10	Mon 6/28/10	289					
291	Remove Applicable Utilities	30 days	Tue 6/15/10	Mon 7/26/10	290FS-10 da					
292	Soil Remediation	191 days	Mon 2/15/10	Mon 11/8/10						

PRELIMINARY DRAFT

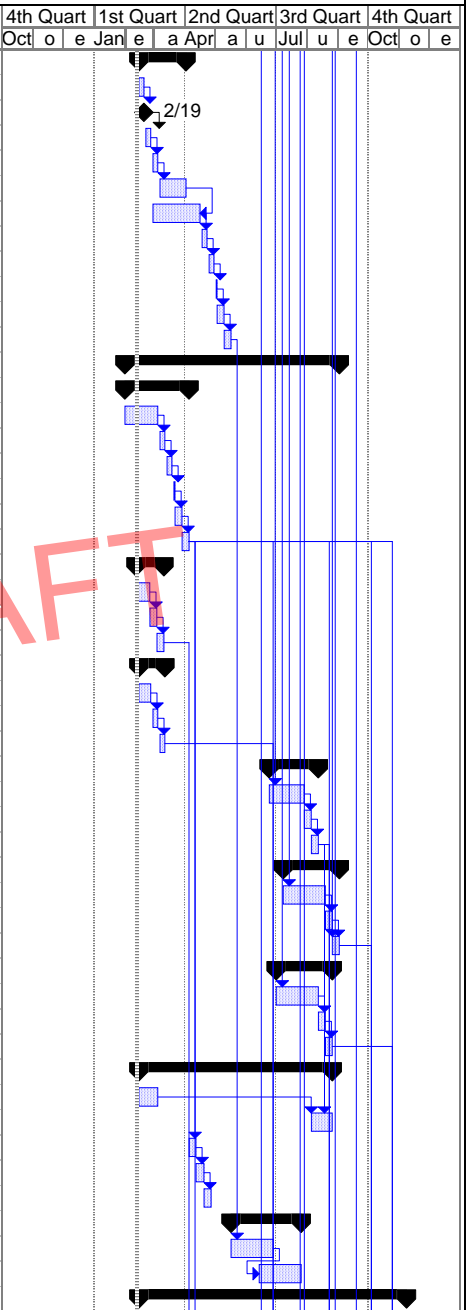


Task		Progress		Summary		External Tasks		Deadline
Split		Milestone		Project Summary		External Milestone		

Tronox Phase B Remediation Program Schedule

February 12, 2010 Preliminary Draft-in-Progress For Discussion Purposes Only

ID	Task Name	Duration	Start	Finish	Predecessor:	4th Quart	1st Quart	2nd Quart	3rd Quart	4th Quart
						Oct o	e Jan e	a Apr a	u Jul u	e Oct o
293	Identify Backfill Source(s)	50 days	Mon 3/1/10	Fri 5/7/10						
294	Identify Potential Sources	20 days	Mon 3/1/10	Fri 3/26/10						
295	"Phase I" Evaluations	20 days	Mon 3/15/10	Fri 4/9/10	294FS-10 da					
296	Soil Certification	20 days	Mon 4/12/10	Fri 5/7/10	295					
297	Soil Sampling and Analysis	20 days	Mon 4/12/10	Fri 5/7/10						
298	Parcels F, G and H	30 days	Mon 2/15/10	Fri 3/26/10						
299	Contractor Selection (any permits needed?)	10 days	Mon 2/15/10	Fri 2/26/10						
300	Notice to Proceed	0 days	Fri 2/26/10	Fri 2/26/10	299					
301	Excavate, Transport to TSDF	10 days	Mon 3/1/10	Fri 3/12/10	300					
302	Collect and Evaluate Confirmation Samples	10 days	Mon 3/15/10	Fri 3/26/10	301					
303	Parcels C and D	20 days	Mon 7/5/10	Fri 7/30/10						
304	Access Open for Remediation	0 days	Mon 7/5/10	Mon 7/5/10						
305	Excavate, Transport to TSDF	10 days	Mon 7/5/10	Fri 7/16/10	304					
306	Collect and Evaluate Confirmation Samples	10 days	Mon 7/19/10	Fri 7/30/10	305					
307	Mn Tailings	60 days	Tue 4/6/10	Mon 6/28/10						
308	Excavate, Transport to TSDF	12 wks	Tue 4/6/10	Mon 6/28/10	262,266					
309	Area I	40 days	Tue 6/29/10	Mon 8/23/10						
310	Excavate, Transport to TSDF	40 days	Tue 6/29/10	Mon 8/23/10	262,270,308					
311	Area II	30 days	Tue 8/24/10	Mon 10/4/10						
312	Excavate, Transport to TSDF	30 days	Tue 8/24/10	Mon 10/4/10	262,274,310					
313	Area IV	15 days	Tue 10/5/10	Mon 10/25/10						
314	Excavate, Transport to TSDF	15 days	Tue 10/5/10	Mon 10/25/10	278,262,312					
315	Area III	10 days	Tue 10/26/10	Mon 11/8/10						
316	Excavate, Transport to TSDF	10 days	Tue 10/26/10	Mon 11/8/10	282,314,262					
317	Data Validation and DVSR Reports	471 days	Wed 4/15/09	Wed 2/2/11						
318	Data Validation Summary Report - Parcels F, G and H	31 days	Mon 3/29/10	Mon 5/10/10						
319	Internal Draft DVSR	11 days	Mon 3/29/10	Mon 4/12/10	302					
320	Client Review/Draft Finalization	5 days	Tue 4/13/10	Mon 4/19/10	319					
321	Submit to NDEP	0 days	Mon 4/19/10	Mon 4/19/10	320					
322	NDEP Review	5 days	Tue 4/20/10	Mon 4/26/10	321					
323	Respond to Comments/DVSR Finalization	10 days	Tue 4/27/10	Mon 5/10/10	322					
324	Data Validation Summary Report - Parcels C and D	31 days	Mon 8/2/10	Mon 9/13/10						
325	Internal Draft DVSR	11 days	Mon 8/2/10	Mon 8/16/10	306					
326	Client Review/Draft Finalization	5 days	Tue 8/17/10	Mon 8/23/10	325					
327	Submit to NDEP	0 days	Mon 8/23/10	Mon 8/23/10	326					
328	NDEP Review	5 days	Tue 8/24/10	Mon 8/30/10	327					
329	Respond to Comments/DVSR Finalization	10 days	Tue 8/31/10	Mon 9/13/10	328					
330	<i>Cap Remaining Impacted Soils</i>	20 days	Wed 4/15/09	Tue 5/12/09						
331	Replace Utility Lines as Necessary	30 days	Wed 5/13/09	Tue 6/23/09	330					
332	Finish Grading Site	30 days	Wed 6/24/09	Tue 8/4/09	331					
333	Construct Surface Drainage Facilities	30 days	Wed 8/5/09	Tue 9/15/09	332					
334	Construction Management/Oversight	222 days	Tue 3/30/10	Wed 2/2/11						
335	Perchlorate Soil Flushing Pilot Test	150 days	Mon 3/1/10	Fri 9/24/10						
336	Pilot Test Workplan	30 days	Mon 3/1/10	Fri 4/9/10						
337	Workplan Preparation	10 days	Mon 3/1/10	Fri 3/12/10						
338	Review Workplan (Tronox, Chartis)	5 days	Mon 3/15/10	Fri 3/19/10	337					
339	Revise and Finalize WP	5 days	Mon 3/22/10	Fri 3/26/10	338					
340	Submit WP to NDEP	0 days	Fri 3/26/10	Fri 3/26/10	339					
341	NDEP Review and Approve WP	5 days	Mon 3/29/10	Fri 4/2/10	340					
342	Column Test	5 days	Mon 4/5/10	Fri 4/9/10	341					

PRELIMINARY DRAFT




Tronox Phase B Remediation Program Schedule

February 12, 2010 Preliminary Draft-in-Progress For Discussion Purposes Only

ID	Task Name	Duration	Start	Finish	Predecessor:	4th Quart	1st Quart	2nd Quart	3rd Quart	4th Quart		
						Oct	e	Jan	e	a	Apr	a
343	Pilot Test Implementation	12 wks	Mon 4/12/10	Fri 7/2/10	341,342							
344	Full Scale	12 wks	Mon 7/5/10	Fri 9/24/10	343							
345	Data Usability Studies	45 days	Mon 7/26/10	Fri 9/24/10	104							
346	Internal Draft Usability Study	20 days	Mon 7/26/10	Fri 8/20/10	104,97FS-25							
347	Client Review/Draft Finalization	5 days	Mon 8/23/10	Fri 8/27/10	346							
348	Submit to NDEP	0 days	Fri 8/27/10	Fri 8/27/10	347							
349	NDEP Review	10 days	Mon 8/30/10	Fri 9/10/10	348							
350	Respond to Comments	5 days	Mon 9/13/10	Fri 9/17/10	349							
351	Data Usability Report Finalization	5 days	Mon 9/20/10	Fri 9/24/10	350							
352	NDEP Meeting	17 days	Mon 9/27/10	Tue 10/19/10								
353	Meeting Prep	5 days	Mon 9/27/10	Fri 10/1/10	351							
354	Client Meeting/Dry Run	1 day	Mon 10/4/10	Mon 10/4/10	353							
355	Agency Meeting	1 day	Tue 10/19/10	Tue 10/19/10	354FS+10 da							
356	Phase B Report	76 days	Fri 6/11/10	Fri 9/24/10								
357	CSM Refinement	20 days	Mon 8/30/10	Fri 9/24/10	97,348							
358	Draft Phase B Report Preparation	20 days	Fri 6/11/10	Thu 7/8/10	175							
359	Client Review/Draft Finalization	10 days	Fri 7/9/10	Thu 7/22/10	358							
360	Submit to NDEP	0 days	Thu 7/22/10	Thu 7/22/10	359							
361	NDEP Review	10 days	Fri 7/23/10	Thu 8/5/10	360							
362	Respond to Comments/Report Finalization	10 days	Fri 8/6/10	Thu 8/19/10	361							
363	Human Health Risk WP	260 days	Mon 1/4/10	Fri 12/31/10								
364	HHRA WP Revisions	23 days	Mon 1/4/10	Wed 2/3/10								
365	HHRA WP Finalization	25 days	Thu 2/4/10	Wed 3/10/10	364							
366	Post Closure Risk Assessment	40 days	Mon 9/20/10	Fri 11/12/10	175,351FS-5							
367	Review RA and (Tronox, Chartis)	10 days	Mon 11/15/10	Fri 11/26/10	366							
368	Revise and Finalize RA	10 days	Mon 11/29/10	Fri 12/10/10	367							
369	Submit RA to NDEP	0 days	Fri 12/10/10	Fri 12/10/10	368							
370	NDEP Review and Approve	15 days	Mon 12/13/10	Fri 12/31/10	369							
371	Soil Vapor Intrusion Evaluation and Mitigation	270 days	Mon 1/4/10	Fri 1/14/11								
372	Evaluate Soil Gas Data	10 days	Mon 1/4/10	Fri 1/15/10								
373	Evaluate Phase B Soil Data	10 days	Mon 1/18/10	Fri 1/29/10	372							
374	Pilot Test	10 days	Mon 3/1/10	Fri 3/12/10	372FS+30 da							
375	System design	15 days	Mon 3/15/10	Fri 4/2/10	374							
376	Obtain Permit	20 days	Mon 4/5/10	Fri 4/30/10	375							
377	Install Sub Slab Depressurization	20 days	Mon 5/3/10	Fri 5/28/10	376							
378	System Start Up	5 days	Mon 5/31/10	Fri 6/4/10	377							
379	Operations and Maintenance	8 mons	Mon 6/7/10	Fri 1/14/11	378							
380	Closure	175 days	Tue 5/11/10	Mon 1/10/11								
381	Parcel F, G and H	55 days	Tue 5/11/10	Mon 7/26/10								
382	Prepare Closure Report	20 days	Tue 5/11/10	Mon 6/7/10	323							
383	Review CR (Tronox, Chartis)	10 days	Tue 6/8/10	Mon 6/21/10	382							
384	Revise and Finalize CR	10 days	Tue 6/22/10	Mon 7/5/10	383							
385	Submit CR to NDEP	0 days	Mon 7/5/10	Mon 7/5/10	384							
386	NDEP Review and Approve CR	15 days	Tue 7/6/10	Mon 7/26/10	385							
387	Parcel C and D	55 days	Tue 9/14/10	Mon 11/29/10								
388	Prepare Closure Report	20 days	Tue 9/14/10	Mon 10/11/10	329							
389	Review CR (Tronox, Chartis)	10 days	Tue 10/12/10	Mon 10/25/10	388							
390	Revise and Finalize CR	10 days	Tue 10/26/10	Mon 11/8/10	389							
391	Submit CR to NDEP	0 days	Mon 11/8/10	Mon 11/8/10	390							
392	NDEP Review and Approve CR	15 days	Tue 11/9/10	Mon 11/29/10	391							

PRELIMINARY DRAFT

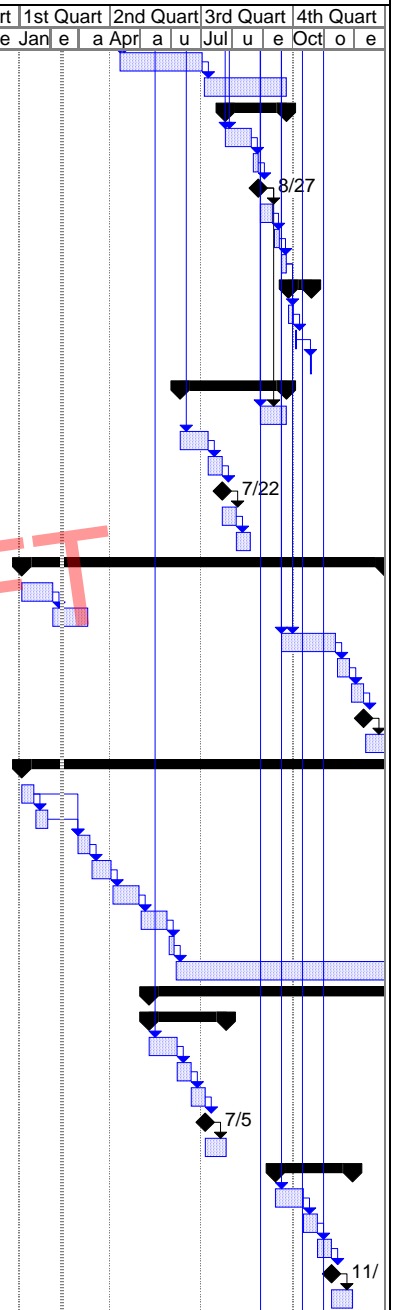


Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

Tronox Phase B Remediation Program Schedule

February 12, 2010 Preliminary Draft-in-Progress For Discussion Purposes Only

ID	Task Name	Duration	Start	Finish	Predecessor:	4th Quart 1st Quart 2nd Quart 3rd Quart 4th Quart												
						Oct	o	e	Jan	e	a	Apr	a	u	Jul	u	e	Oct
393	Area I	55 days	Tue 8/24/10	Mon 11/8/10														
394	Prepare Closure Report	20 days	Tue 8/24/10	Mon 9/20/10	310													
395	Review CR (Tronox, Chartis)	10 days	Tue 9/21/10	Mon 10/4/10	394													
396	Revise and Finalize CR	10 days	Tue 10/5/10	Mon 10/18/10	395													
397	Submit CR to NDEP	0 days	Mon 10/18/10	Mon 10/18/10	396													
398	NDEP Review and Approve CR	15 days	Tue 10/19/10	Mon 11/8/10	397													
399	Area II	55 days	Tue 10/5/10	Mon 12/20/10														
400	Prepare Closure Report	20 days	Tue 10/5/10	Mon 11/1/10	312													
401	Review CR (Tronox, Chartis)	10 days	Tue 11/2/10	Mon 11/15/10	400													
402	Revise and Finalize CR	10 days	Tue 11/16/10	Mon 11/29/10	401													
403	Submit CR to NDEP	0 days	Mon 11/29/10	Mon 11/29/10	402													
404	NDEP Review and Approve CR	15 days	Tue 11/30/10	Mon 12/20/10	403													
405	Area IV	55 days	Tue 10/26/10	Mon 1/10/11														
406	Prepare Closure Report	20 days	Tue 10/26/10	Mon 11/22/10	314													
407	Review CR (Tronox, Chartis)	10 days	Tue 11/23/10	Mon 12/6/10	406													
408	Revise and Finalize CR	10 days	Tue 12/7/10	Mon 12/20/10	407													
409	Submit CR to NDEP	0 days	Mon 12/20/10	Mon 12/20/10	408													
410	NDEP Review and Approve CR	15 days	Tue 12/21/10	Mon 1/10/11	409													



PRELIMINARY DRAFT

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
