


Tronox Phase B Remediation Program Schedule

February 16, 2010

Work-in-Progress

ID	Task Name	Duration	Start	Finish	Predecessor:	Q4							Q1			Q2			Q3			Q4				
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D						
1	Phase B Program	499 days	Wed 4/15/09	Mon 3/14/11																						
2	Finalize Phase B Site Investigation	447 days	Wed 4/15/09	Thu 12/30/10																						
3	PM/Client/Agency Coordination	436 days	Mon 4/20/09	Mon 12/20/10																						
4	Weekly Status Calls	436 days	Mon 4/20/09	Mon 12/20/10																						
92	Data Mgmt/Validation	447 days	Wed 4/15/09	Thu 12/30/10																						
93	Database Management	447 days	Wed 4/15/09	Thu 12/30/10																						
94	Source Area I Laboratory Data Validation	25 days	Fri 10/16/09	Thu 11/19/09																						
95	Source Area II Laboratory Data Validation	43 days	Wed 11/18/09	Fri 1/15/10																						
96	Source Area IV Laboratory Data Validation	35 days	Wed 12/16/09	Tue 2/2/10																						
97	Source Area III Laboratory Data Validation	24 days	Thu 12/31/09	Tue 2/2/10																						
98	NDEP Phase B Source Area Meetings	15 days	Mon 1/18/10	Fri 2/5/10																						
99	NDEP Meeting	15 days	Mon 1/18/10	Fri 2/5/10																						
100	Meeting Material Preparation	14 days	Mon 1/18/10	Thu 2/4/10	95																					
101	Agency Meeting	1 day	Fri 2/5/10	Fri 2/5/10	100																					
102	Phase B Reporting	82 days	Fri 11/20/09	Mon 3/15/10																						
103	Data Validation Summary Report - Area 1	41 days	Fri 11/20/09	Fri 1/15/10																						
109	Data Validation Summary Report - Area II	35 days	Mon 1/18/10	Fri 3/5/10																						
110	Internal Draft DVSR	17 days	Mon 1/18/10	Tue 2/9/10	95																					
111	Client Review/Draft Finalization	3 days	Wed 2/10/10	Fri 2/12/10	110																					
112	Submit to NDEP	0 days	Fri 2/12/10	Fri 2/12/10	111																					
113	NDEP Review	5 days	Mon 2/15/10	Fri 2/19/10	112																					
114	Respond to Comments/DVSR Finalization	10 days	Mon 2/22/10	Fri 3/5/10	113																					
115	Data Validation Summary Report - Area IV	28 days	Wed 2/3/10	Fri 3/12/10																						
116	Internal Draft DVSR	12 days	Wed 2/3/10	Thu 2/18/10	96																					
117	Client Review/Draft Finalization	1 day	Fri 2/19/10	Fri 2/19/10	116																					
118	Submit to NDEP	0 days	Fri 2/19/10	Fri 2/19/10	117																					
119	NDEP Review	5 days	Mon 2/22/10	Fri 2/26/10	118																					
120	Respond to Comments/DVSR Finalization	10 days	Mon 3/1/10	Fri 3/12/10	119																					
121	Data Validation Summary Report - Area III	28 days	Wed 2/3/10	Fri 3/12/10																						
122	Internal Draft DVSR	11 days	Wed 2/3/10	Wed 2/17/10	97																					
123	Client Review/Draft Finalization	2 days	Thu 2/18/10	Fri 2/19/10	122																					
124	Submit to NDEP	0 days	Fri 2/19/10	Fri 2/19/10	123																					
125	NDEP Review	5 days	Mon 2/22/10	Fri 2/26/10	124																					
126	Respond to Comments/DVSR Finalization	10 days	Mon 3/1/10	Fri 3/12/10	125																					
127	Data Validation Summary Report - Groundwater	29 days	Wed 2/3/10	Mon 3/15/10																						
128	Internal Draft DVSR	12 days	Wed 2/3/10	Thu 2/18/10	97																					
129	Client Review/Draft Finalization	2 days	Fri 2/19/10	Mon 2/22/10	128																					
130	Submit to NDEP	0 days	Mon 2/22/10	Mon 2/22/10	129																					
131	NDEP Review	5 days	Tue 2/23/10	Mon 3/1/10	130																					
132	Respond to Comments/DVSR Finalization	10 days	Tue 3/2/10	Mon 3/15/10	131																					
133	Remediation Planning	59 days	Mon 12/7/09	Thu 2/25/10																						
134	Conceptual Remediation Planning/Prelim Risk Eval	59 days	Mon 12/7/09	Thu 2/25/10																						
135	Area 1	41 days	Mon 12/7/09	Mon 2/1/10																						
136	Area II	15 days	Mon 1/18/10	Fri 2/5/10	95																					
137	Area IV	17 days	Wed 2/3/10	Thu 2/25/10	96																					
138	Area III	17 days	Wed 2/3/10	Thu 2/25/10	97																					
139	Phase B Remediation Characterization Sampling	177 days	Mon 11/23/09	Tue 7/27/10																						
140	Area I	43 days	Mon 11/23/09	Wed 1/20/10																						

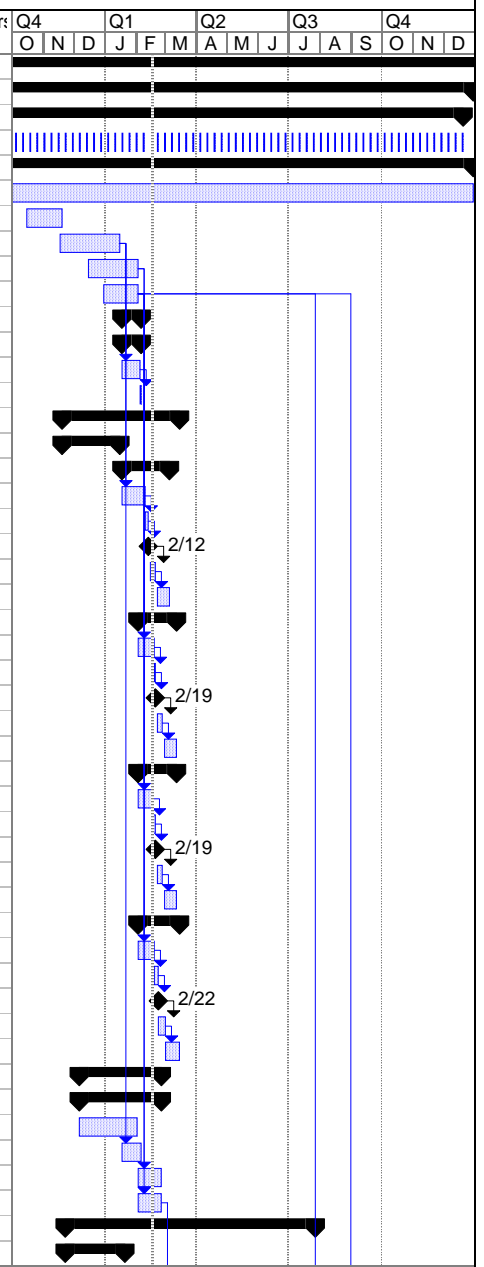

Task Progress Summary External Tasks Deadline


Split Milestone Project Summary External Milestone

Tronox Phase B Remediation Program Schedule

February 16, 2010

Work-in-Progress

ID	Task Name	Duration	Start	Finish	Predecessor:	Q4		Q1			Q2		Q3			Q4	
						O	N	D	J	F	M	A	M	J	J	A	S
285	Review Bids and Award Contract	5 days	Tue 3/30/10	Mon 4/5/10	284												
286	Mn Tailings	20 days	Fri 2/12/10	Thu 3/11/10													
287	Prepare Remediation Plans and Specifications	10 days	Fri 2/12/10	Thu 2/25/10													
288	Review Plans and Specifications (Tronox, Chartis)	5 days	Fri 2/26/10	Thu 3/4/10	287												
289	Issue Plans and Specifications	5 days	Fri 3/5/10	Thu 3/11/10	288												
290	Area IV	20 days	Wed 5/19/10	Tue 6/15/10													
291	Prepare Remediation Plans and Specifications	10 days	Wed 5/19/10	Tue 6/1/10	244												
292	Review Plans and Specifications (Tronox, Chartis)	5 days	Wed 6/2/10	Tue 6/8/10	291												
293	Issue Plans and Specifications	5 days	Wed 6/9/10	Tue 6/15/10	292												
294	Area III	20 days	Tue 6/29/10	Mon 7/26/10													
295	Prepare Remediation Plans and Specifications	10 days	Tue 6/29/10	Mon 7/12/10	251												
296	Review Plans and Specifications (Tronox, Chartis)	5 days	Tue 7/13/10	Mon 7/19/10	295												
297	Issue Plans and Specifications	5 days	Tue 7/20/10	Mon 7/26/10	296												
298	Area II	20 days	Tue 7/6/10	Mon 8/2/10													
299	Prepare Remediation Plans and Specifications	10 days	Tue 7/6/10	Mon 7/19/10	257												
300	Review Plans and Specifications (Tronox, Chartis)	5 days	Tue 7/20/10	Mon 7/26/10	299												
301	Issue Plans and Specifications	5 days	Tue 7/27/10	Mon 8/2/10	300,251												
302	Area I	40 days	Tue 6/22/10	Mon 8/16/10													
303	Prepare Remediation Plans and Specifications	30 days	Tue 6/22/10	Mon 8/2/10	263												
304	Review Plans and Specifications (Tronox, Chartis)	5 days	Tue 8/3/10	Mon 8/9/10	303												
305	Issue Plans and Specifications	5 days	Tue 8/10/10	Mon 8/16/10	304												
306	Grading and Dust Monitoring Permit	121 days	Mon 2/22/10	Mon 8/9/10													
307	Parcels C, D, F, G, and H	15 days	Mon 2/22/10	Fri 3/12/10													
308	Permits - Mn Tailings	15 days	Mon 3/8/10	Fri 3/26/10													
309	Permits - Other Areas	15 days	Tue 7/20/10	Mon 8/9/10	297FS-5 day												
310	Contractor Submits Grading and DMP	5 days	Tue 4/6/10	Mon 4/12/10	285												
311	Clark County Review/Permitting	10 days	Tue 4/13/10	Mon 4/26/10	310												
312	Issue Permits	5 days	Tue 4/27/10	Mon 5/3/10	311												
313	Demolition	50 days	Tue 5/18/10	Mon 7/26/10													
314	Demolish Applicable Bldgs	30 days	Tue 5/18/10	Mon 6/28/10	277												
315	Remove Applicable Utilities	30 days	Tue 6/15/10	Mon 7/26/10	314FS-10 da												
316	Soil Remediation	221 days	Mon 2/15/10	Mon 12/20/10													
317	Identify Backfill Source(s)	50 days	Mon 3/1/10	Fri 5/7/10													
318	Identify Potential Sources	20 days	Mon 3/1/10	Fri 3/26/10													
319	"Phase I" Evaluations	20 days	Mon 3/15/10	Fri 4/9/10	318FS-10 da												
320	Soil Certification	20 days	Mon 4/12/10	Fri 5/7/10	319												
321	Soil Sampling and Analysis	20 days	Mon 4/12/10	Fri 5/7/10													
322	Implementation of SWPPP Measures	45 days	Tue 5/4/10	Mon 7/5/10	312												
323	Parcels C, D, F, G and H	50 days	Mon 2/15/10	Fri 4/23/10													
324	Contractor Selection	10 days	Mon 2/15/10	Fri 2/26/10													
325	Notice to Proceed	0 days	Fri 2/26/10	Fri 2/26/10	324												
326	Excavate, Transport to TSDF	10 days	Mon 3/15/10	Fri 3/26/10	325,307												
327	Collect and Evaluate Confirmation Samples	20 days	Mon 3/29/10	Fri 4/23/10	326												
328	Mn Tailings	60 days	Tue 4/6/10	Mon 6/28/10													
329	Excavate, Transport to TSDF	12 wks	Tue 4/6/10	Mon 6/28/10	285,289,307												
330	Area IV	15 days	Tue 6/29/10	Mon 7/19/10													
331	Excavate, Transport to TSDF	15 days	Tue 6/29/10	Mon 7/19/10	285,293,329,												
332	Area III	15 days	Tue 7/27/10	Mon 8/16/10													

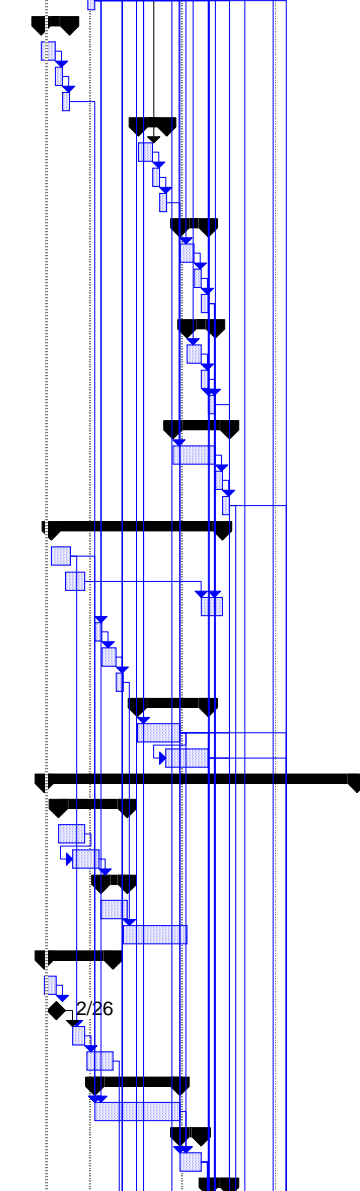

Task Progress Summary External Tasks Deadline


 Split Milestone Project Summary External Milestone

Tronox Phase B Remediation Program Schedule

February 16, 2010

Work-in-Progress

ID	Task Name	Duration	Start	Finish	Predecessor:	Q4				Q1			Q2			Q3			Q4		
						O	N	D		J	F	M	A	M	J	J	A	S	O	N	D
333	Excavate, Transport to TSDF	15 days	Tue 7/27/10	Mon 8/16/10	285,297,331,																
334	Area II	40 days	Tue 8/17/10	Mon 10/11/10																	
335	Excavate, Transport to TSDF	40 days	Tue 8/17/10	Mon 10/11/10	301,285,333,																
336	Area I	50 days	Tue 10/12/10	Mon 12/20/10																	
337	Excavate, Transport to TSDF	50 days	Tue 10/12/10	Mon 12/20/10	305,335,285,																
338	Data Validation and DVSR Reports	35 days	Mon 4/26/10	Fri 6/11/10																	
339	Data Validation Summary Report - Parcels C, D, F, G and H	35 days	Mon 4/26/10	Fri 6/11/10																	
340	Internal Draft DVSR	15 days	Mon 4/26/10	Fri 5/14/10	327																
341	Client Review/Draft Finalization	5 days	Mon 5/17/10	Fri 5/21/10	340																
342	Submit to NDEP	0 days	Fri 5/21/10	Fri 5/21/10	341																
343	NDEP Review	5 days	Mon 5/24/10	Fri 5/28/10	342																
344	Respond to Comments/DVSR Finalization	10 days	Mon 5/31/10	Fri 6/11/10	343																
345	Replace Utility Lines as Necessary	130 days	Tue 7/20/10	Mon 1/17/11																	
346	Area IV	20 days	Tue 7/20/10	Mon 8/16/10	331																
347	Area III	20 days	Tue 8/17/10	Mon 9/13/10	333																
348	Area II	20 days	Tue 10/12/10	Mon 11/8/10	335																
349	Area I	20 days	Tue 12/21/10	Mon 1/17/11	337																
350	Institutional Controls/Environmental Covenants	161 days	Mon 7/5/10	Mon 2/14/11																	
351	<i>Develop IC Plan</i>	60 days	Mon 7/5/10	Fri 9/24/10																	
352	<i>Develop Risk Management Plan</i>	60 days	Mon 7/12/10	Fri 10/1/10																	
353	<i>Cap Pond Berms</i>	30 days	Tue 8/17/10	Mon 9/27/10	305																
354	Cap Remaining Impacted Soils -if necessary	130 days	Tue 8/17/10	Mon 2/14/11																	
355	Area IV	20 days	Tue 8/17/10	Mon 9/13/10	346																
356	Area III	20 days	Tue 9/14/10	Mon 10/11/10	347																
357	Area II	20 days	Tue 11/9/10	Mon 12/6/10	348																
358	Area I	20 days	Tue 1/18/11	Mon 2/14/11	349																
359	Finish Grading Site	130 days	Tue 9/14/10	Mon 3/14/11																	
360	Area IV	20 days	Tue 9/14/10	Mon 10/11/10	355																
361	Area III	20 days	Tue 10/12/10	Mon 11/8/10	356																
362	Area II	20 days	Tue 12/7/10	Mon 1/3/11	357																
363	Area I	20 days	Tue 2/15/11	Mon 3/14/11	358																
364	<i>Construction Management/Oversight</i>	220 days	Tue 5/11/10	Mon 3/14/11	276																
365	Perchlorate Soil Flushing Pilot Test	222 days	Mon 3/1/10	Tue 1/4/11																	
366	Pilot Test Workplan	52 days	Mon 3/1/10	Tue 5/11/10																	
367	<i>Workplan Preparation</i>	10 days	Mon 3/1/10	Fri 3/12/10																	
368	<i>Review Workplan (Tronox, Chartis)</i>	5 days	Mon 3/15/10	Fri 3/19/10	367																
369	<i>Revise and Finalize WP</i>	5 days	Mon 3/22/10	Fri 3/26/10	368																
370	<i>Submit WP to NDEP</i>	0 days	Fri 3/26/10	Fri 3/26/10	369																
371	<i>NDEP Review</i>	5 days	Mon 3/29/10	Fri 4/2/10	370																
372	<i>Respond to Comments/WP Finalization</i>	10 days	Mon 4/5/10	Fri 4/16/10	371																
373	<i>NDEP Approval</i>	2 days	Mon 4/19/10	Tue 4/20/10	372																
374	<i>Column Test</i>	15 days	Tue 4/20/10	Tue 5/11/10	373																
375	<i>Contractor Selection</i>	10 days	Wed 4/21/10	Tue 5/4/10	367																
376	<i>Notice to Proceed</i>	0 days	Tue 4/20/10	Tue 4/20/10	373																
377	<i>Implementation</i>	15 days	Wed 4/21/10	Tue 5/11/10																	
378	<i>Pilot Test Implementation</i>	12 wks	Wed 5/12/10	Tue 8/3/10	371,374																
379	<i>Full Scale</i>	22 wks	Wed 8/4/10	Tue 1/4/11	378																
380	Data Usability Studies	45 days	Wed 7/28/10	Tue 9/28/10	104																

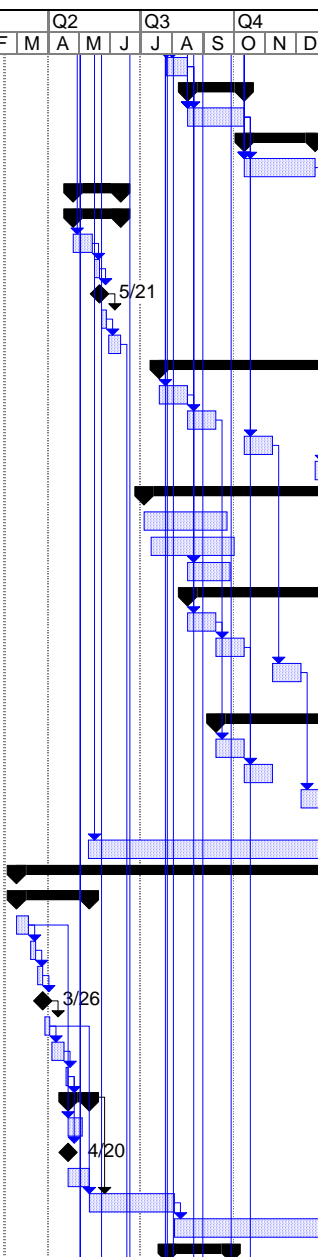


Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

Tronox Phase B Remediation Program Schedule

February 16, 2010

Work-in-Progress

ID	Task Name	Duration	Start	Finish	Predecessor:	Q4		Q1			Q2		Q3			Q4		
						O	N	D	J	F	M	A	M	J	J	A	S	O
381	Internal Draft Usability Study	20 days	Wed 7/28/10	Tue 8/24/10	104,97FS-25													
382	Client Review/Draft Finalization	5 days	Wed 8/25/10	Tue 8/31/10	381													
383	Submit to NDEP	0 days	Tue 8/31/10	Tue 8/31/10	382													
384	NDEP Review	10 days	Wed 9/1/10	Tue 9/14/10	383													
385	Respond to Comments	5 days	Wed 9/15/10	Tue 9/21/10	384													
386	Data Usability Report Finalization	5 days	Wed 9/22/10	Tue 9/28/10	385													
387	Development of Decision Units	10 days	Wed 9/29/10	Tue 10/12/10	386,197													
388	NDEP Meeting	17 days	Wed 10/13/10	Thu 11/4/10														
389	Meeting Prep	5 days	Wed 10/13/10	Tue 10/19/10	387													
390	Client Meeting/Dry Run	1 day	Wed 10/20/10	Wed 10/20/10	389													
391	Agency Meeting	1 day	Thu 11/4/10	Thu 11/4/10	390FS+10 da													
392	Phase B Report	76 days	Tue 6/15/10	Tue 9/28/10														
393	CSM Refinement	20 days	Wed 9/1/10	Tue 9/28/10	97,383													
394	<i>Draft Phase B Report Preparation</i>	<i>20 days</i>	<i>Tue 6/15/10</i>	<i>Mon 7/12/10</i>	<i>197</i>													
395	Client Review/Draft Finalization	10 days	Tue 7/13/10	Mon 7/26/10	394													
396	Submit to NDEP	0 days	Mon 7/26/10	Mon 7/26/10	395													
397	NDEP Review	10 days	Tue 7/27/10	Mon 8/9/10	396													
398	Respond to Comments/Report Finalization	10 days	Tue 8/10/10	Mon 8/23/10	397													
399	Human Health Risk WP	236 days	Wed 4/15/09	Wed 3/10/10														
400	HHRA WP Revisions	23 days	Mon 1/4/10	Wed 2/3/10														
401	HHRA WP Finalization	25 days	Thu 2/4/10	Wed 3/10/10	400													
402	Review WP and (Tronox, Chartis)	10 days	Wed 4/15/09	Tue 4/28/09														
403	Revise and Finalize RA	5 days	Wed 4/29/09	Tue 5/5/09	402													
404	Submit WP to NDEP	0 days	Tue 5/5/09	Tue 5/5/09	403													
405	NDEP Review and Approve	10 days	Wed 5/6/09	Tue 5/19/09	404													
406	Probabilistic HHRA (PRA) WP	45 days	Thu 3/11/10	Wed 5/12/10														
407	PRA Development	10 days	Thu 3/11/10	Wed 3/24/10	401													
408	Review PRA and (Tronox, Chartis)	10 days	Thu 3/25/10	Wed 4/7/10	407													
409	Revise and Finalize PRA	10 days	Thu 4/8/10	Wed 4/21/10	408													
410	Submit PRA to NDEP	0 days	Wed 4/21/10	Wed 4/21/10	409													
411	NDEP Review and Approve	15 days	Thu 4/22/10	Wed 5/12/10	410													
412	Human Health Risk Assessment	55 days	Tue 4/27/10	Mon 7/12/10														
413	Alternative BCL Development	20 days	Tue 5/18/10	Mon 6/14/10	175													
414	Post Closure Risk Assessment	55 days	Tue 4/27/10	Mon 7/12/10														
415	<i>Area IV - will actually be based on DU's once developed</i>	<i>55 days</i>	<i>Tue 4/27/10</i>	<i>Mon 7/12/10</i>														
416	Prepare HHRA	20 days	Tue 4/27/10	Mon 5/24/10	195													
417	Review RA (Tronox, Chartis)	10 days	Tue 5/25/10	Mon 6/7/10	416													
418	Revise and Finalize CR	10 days	Tue 6/8/10	Mon 6/21/10	417													
419	Submit RA to NDEP	0 days	Mon 6/21/10	Mon 6/21/10	418													
420	NDEP Review and Approve RA	15 days	Tue 6/22/10	Mon 7/12/10	419													
421	<i>Area II - will actually be based on DU's once developed</i>	<i>55 days</i>	<i>Tue 4/27/10</i>	<i>Mon 7/12/10</i>														
422	Prepare HHRA	20 days	Tue 4/27/10	Mon 5/24/10	195													
423	Review RA (Tronox, Chartis)	10 days	Tue 5/25/10	Mon 6/7/10	422													
424	Revise and Finalize CR	10 days	Tue 6/8/10	Mon 6/21/10	423													
425	Submit RA to NDEP	0 days	Mon 6/21/10	Mon 6/21/10	424													
426	NDEP Review and Approve RA	15 days	Tue 6/22/10	Mon 7/12/10	425													
427	<i>Area I - will actually be based on DU's once developed</i>	<i>55 days</i>	<i>Tue 4/27/10</i>	<i>Mon 7/12/10</i>														
428	Prepare HHRA	20 days	Tue 4/27/10	Mon 5/24/10	195													

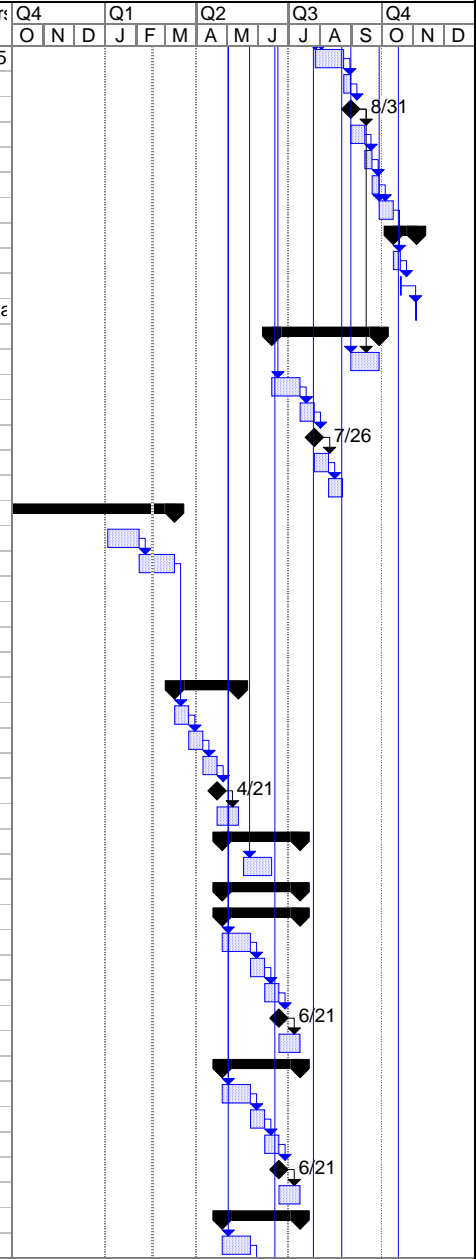

Task	Progress	Summary	External Tasks	Deadline	
Split	Milestone	Project Summary	External Milestone		

Tronox Phase B Remediation Program Schedule

February 16, 2010

Work-in-Progress

ID	Task Name	Duration	Start	Finish	Predecessor	Quarter															
						Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4							
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	
429	Review RA (Tronox, Chartis)	10 days	Tue 5/25/10	Mon 6/7/10	428																
430	Revise and Finalize CR	10 days	Tue 6/8/10	Mon 6/21/10	429																
431	Submit RA to NDEP	0 days	Mon 6/21/10	Mon 6/21/10	430																
432	NDEP Review and Approve RA	15 days	Tue 6/22/10	Mon 7/12/10	431																
433	Soil Vapor Intrusion Evaluation and Mitigation	110 days	Mon 1/4/10	Fri 6/4/10																	
434	Evaluate Soil Gas Data	10 days	Mon 1/4/10	Fri 1/15/10																	
435	Evaluate Phase B Soil Data	10 days	Mon 1/18/10	Fri 1/29/10	434																
436	Pilot Test	10 days	Mon 3/1/10	Fri 3/12/10	434FS+30 da																
437	System design	15 days	Mon 3/15/10	Fri 4/2/10	436																
438	Obtain Permit	20 days	Mon 4/5/10	Fri 4/30/10	437																
439	Install Sub Slab Depressurization	20 days	Mon 5/3/10	Fri 5/28/10	438																
440	System Start Up	5 days	Mon 5/31/10	Fri 6/4/10	439																
441	Operations and Maintenance (not scheduled)	0 days	Fri 6/4/10	Fri 6/4/10	440																
442	Closures	141 days	Mon 6/14/10	Mon 12/27/10																	
443	Parcel C, D, F, G and H	55 days	Mon 6/14/10	Fri 8/27/10																	
444	Prepare Closure Report	20 days	Mon 6/14/10	Fri 7/9/10	344																
445	Review CR (Tronox, Chartis)	10 days	Mon 7/12/10	Fri 7/23/10	444																
446	Revise and Finalize CR	10 days	Mon 7/26/10	Fri 8/6/10	445																
447	Submit CR to NDEP	0 days	Fri 8/6/10	Fri 8/6/10	446																
448	NDEP Review and Approve CR	15 days	Mon 8/9/10	Fri 8/27/10	447																
449	Area IV - will actually be based on decision units once developed	55 days	Tue 7/20/10	Mon 10/4/10																	
450	Prepare Closure Report	20 days	Tue 7/20/10	Mon 8/16/10	331																
451	Review CR (Tronox, Chartis)	10 days	Tue 8/17/10	Mon 8/30/10	450																
452	Revise and Finalize CR	10 days	Tue 8/31/10	Mon 9/13/10	451																
453	Submit CR to NDEP	0 days	Mon 9/13/10	Mon 9/13/10	452																
454	NDEP Review and Approve CR	15 days	Tue 9/14/10	Mon 10/4/10	453																
455	Area II - will actually be based on decision units once developed	55 days	Tue 8/17/10	Mon 11/1/10																	
456	Prepare Closure Report	20 days	Tue 8/17/10	Mon 9/13/10	333																
457	Review CR (Tronox, Chartis)	10 days	Tue 9/14/10	Mon 9/27/10	456																
458	Revise and Finalize CR	10 days	Tue 9/28/10	Mon 10/11/10	457																
459	Submit CR to NDEP	0 days	Mon 10/11/10	Mon 10/11/10	458																
460	NDEP Review and Approve CR	15 days	Tue 10/12/10	Mon 11/1/10	459																
461	Area I - will actually be based on decision units once developed	55 days	Tue 10/12/10	Mon 12/27/10																	
462	Prepare Closure Report	20 days	Tue 10/12/10	Mon 11/8/10	335																
463	Review CR (Tronox, Chartis)	10 days	Tue 11/9/10	Mon 11/22/10	462																
464	Revise and Finalize CR	10 days	Tue 11/23/10	Mon 12/6/10	463																
465	Submit CR to NDEP	0 days	Mon 12/6/10	Mon 12/6/10	464																
466	NDEP Review and Approve CR	15 days	Tue 12/7/10	Mon 12/27/10	465																

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone
