


Tronox Phase B Remediation Program Schedule

February 18, 2010

For NDEP Review

ID	Task Name	Duration	Start	Finish	Predecessors	2010				
						Q4	Q1	Q2	Q3	Q4
1	Phase B Program	455 days	Wed 4/15/09	Tue 1/11/11						
2	Finalize Phase B Site Investigation	447 days	Wed 4/15/09	Thu 12/30/10						
3	PM/Client/Agency Coordination	436 days	Mon 4/20/09	Mon 12/20/10						
4	Weekly Status Calls	436 days	Mon 4/20/09	Mon 12/20/10						
92	Data Mgmt/Validation	447 days	Wed 4/15/09	Thu 12/30/10						
93	Database Management	447 days	Wed 4/15/09	Thu 12/30/10						
94	Source Area I Laboratory Data Validation	25 days	Fri 10/16/09	Thu 11/19/09						
95	Source Area II Laboratory Data Validation	43 days	Wed 11/18/09	Fri 1/15/10						
96	Source Area IV Laboratory Data Validation	35 days	Wed 12/16/09	Tue 2/2/10						
97	Source Area III Laboratory Data Validation	24 days	Thu 12/31/09	Tue 2/2/10						
98	NDEP Phase B Source Area Meetings	15 days	Mon 1/18/10	Fri 2/5/10						
99	NDEP Meeting	15 days	Mon 1/18/10	Fri 2/5/10						
100	Meeting Material Preparation	14 days	Mon 1/18/10	Thu 2/4/10	95					
101	Agency Meeting	1 day	Fri 2/5/10	Fri 2/5/10	100					
102	Phase B Reporting	82 days	Fri 11/20/09	Mon 3/15/10						
103	Data Validation Summary Report - Area 1	41 days	Fri 11/20/09	Fri 1/15/10						
109	Data Validation Summary Report - Area II	35 days	Mon 1/18/10	Fri 3/5/10						
110	Internal Draft DVSR	17 days	Mon 1/18/10	Tue 2/9/10	95					
111	Client Review/Draft Finalization	3 days	Wed 2/10/10	Fri 2/12/10	110					
112	Submit to NDEP	0 days	Fri 2/12/10	Fri 2/12/10	111					
113	NDEP Review	5 days	Mon 2/15/10	Fri 2/19/10	112					
114	Respond to Comments/DVSR Finalization	10 days	Mon 2/22/10	Fri 3/5/10	113					
115	Data Validation Summary Report - Area IV	28 days	Wed 2/3/10	Fri 3/12/10						
116	Internal Draft DVSR	12 days	Wed 2/3/10	Thu 2/18/10	96					
117	Client Review/Draft Finalization	1 day	Fri 2/19/10	Fri 2/19/10	116					
118	Submit to NDEP	0 days	Fri 2/19/10	Fri 2/19/10	117					
119	NDEP Review	5 days	Mon 2/22/10	Fri 2/26/10	118					
120	Respond to Comments/DVSR Finalization	10 days	Mon 3/1/10	Fri 3/12/10	119					
121	Data Validation Summary Report - Area III	28 days	Wed 2/3/10	Fri 3/12/10						
122	Internal Draft DVSR	11 days	Wed 2/3/10	Wed 2/17/10	97					
123	Client Review/Draft Finalization	2 days	Thu 2/18/10	Fri 2/19/10	122					
124	Submit to NDEP	0 days	Fri 2/19/10	Fri 2/19/10	123					
125	NDEP Review	5 days	Mon 2/22/10	Fri 2/26/10	124					
126	Respond to Comments/DVSR Finalization	10 days	Mon 3/1/10	Fri 3/12/10	125					
127	Data Validation Summary Report - Groundwater	29 days	Wed 2/3/10	Mon 3/15/10						
128	Internal Draft DVSR	12 days	Wed 2/3/10	Thu 2/18/10	97					
129	Client Review/Draft Finalization	2 days	Fri 2/19/10	Mon 2/22/10	128					
130	Submit to NDEP	0 days	Mon 2/22/10	Mon 2/22/10	129					
131	NDEP Review	5 days	Tue 2/23/10	Mon 3/1/10	130					
132	Respond to Comments/DVSR Finalization	10 days	Tue 3/2/10	Mon 3/15/10	131					
133	Remediation Planning	59 days	Mon 12/7/09	Thu 2/25/10						
134	Conceptual Remediation Planning/Prelim Risk Eval	59 days	Mon 12/7/09	Thu 2/25/10						
135	Area 1	41 days	Mon 12/7/09	Mon 2/1/10						
136	Area II	15 days	Mon 1/18/10	Fri 2/5/10	95					
137	Area IV	17 days	Wed 2/3/10	Thu 2/25/10	96					
138	Area III	17 days	Wed 2/3/10	Thu 2/25/10	97					
139	Phase B Remediation Supplemental Sampling	173 days	Mon 11/23/09	Wed 7/21/10						
140	Area I	43 days	Mon 11/23/09	Wed 1/20/10						

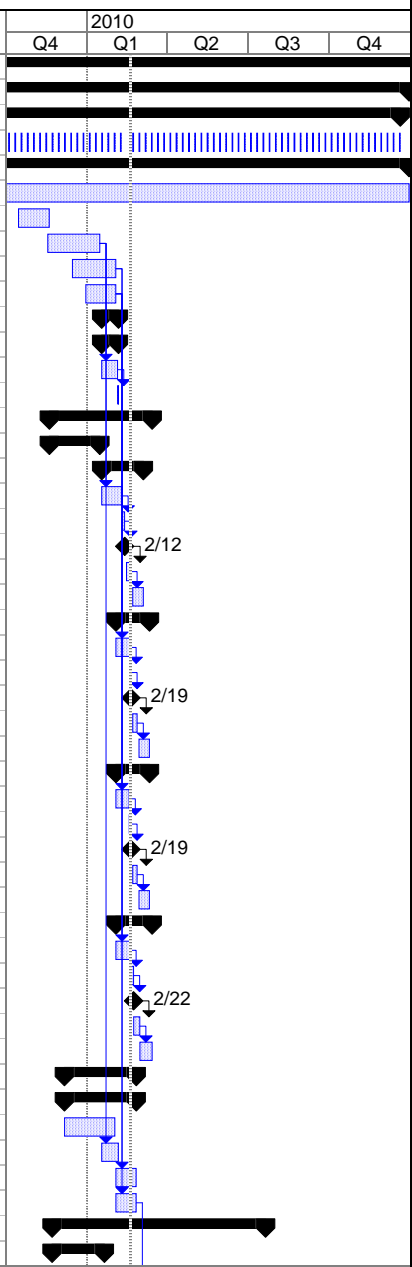

Task Progress Summary External Tasks Deadline


Split Milestone Project Summary External Milestone

Tronox Phase B Remediation Program Schedule

February 18, 2010

For NDEP Review

ID	Task Name	Duration	Start	Finish	Predecessors	2010				
						Q4	Q1	Q2	Q3	Q4
141	Field Coordination/GBP	10 days	Mon 11/23/09	Fri 12/4/09						
142	Field Sampling	3 days	Mon 12/7/09	Wed 12/9/09	141					
143	Laboratory Analysis	30 days	Thu 12/10/09	Wed 1/20/10	142					
144	Area II	49 days	Mon 12/7/09	Thu 2/11/10						
145	Field Coordination/GBP	5 days	Mon 12/7/09	Fri 12/11/09	141					
146	Field Sampling	4 days	Mon 12/14/09	Thu 12/17/09	142SS,145					
147	Laboratory Analysis	30 days	Fri 12/18/09	Thu 1/28/10	146					
148	TCLP Analysis	10 days	Fri 1/29/10	Thu 2/11/10	147					
149	Submittal of Analysis Profile to Landfills	0 days	Thu 2/11/10	Thu 2/11/10	148					
150	Acceptance of Profile Information by Landfills	20 days	Fri 2/12/10	Thu 3/11/10	149					
151	Data Validation and Summary Report (Supplemental Sampling)	37 days	Mon 2/15/10	Tue 4/6/10						
152	Submittal of EDDs to NDEP/Neptune	0 days	Mon 2/15/10	Mon 2/15/10	143,147					
153	Data Validation	10 days	Mon 2/15/10	Fri 2/26/10	152					
154	Draft DVSR	10 days	Mon 3/1/10	Fri 3/12/10	153					
155	Client Review/Draft Finalization	2 days	Mon 3/15/10	Tue 3/16/10	154					
156	Submit to NDEP	0 days	Tue 3/16/10	Tue 3/16/10	155					
157	NDEP Review	5 days	Wed 3/17/10	Tue 3/23/10	156					
158	Respond to Comments/DVSR Finalization	10 days	Wed 3/24/10	Tue 4/6/10	157					
159	Dioxin TEQ Bioaccessability Study	44 days	Mon 2/1/10	Thu 4/1/10						
160	Protocol Development	9 days	Mon 2/1/10	Thu 2/11/10						
161	NDEP Review and Comments	3 days	Fri 2/12/10	Tue 2/16/10	160					
162	Respond to NDEP comments	3 days	Wed 2/17/10	Fri 2/19/10	161					
163	Respond to Comments/WP Finalization	6 days	Mon 2/22/10	Mon 3/1/10	162					
164	NDEP Approval	0 days	Mon 3/1/10	Mon 3/1/10	163					
165	Field Work	8 days	Tue 3/2/10	Thu 3/11/10						
166	Field Coordination/GBP	5 days	Tue 3/2/10	Mon 3/8/10	164					
167	Field Sampling	3 days	Tue 3/9/10	Thu 3/11/10	166					
168	Laboratory Analysis (data validation not required as approved by NDEP)	15 days	Fri 3/12/10	Thu 4/1/10	167					
169	8290 Analysis	10 days	Fri 3/12/10	Thu 3/25/10						
170	In-Vitro Analysis	5 days	Fri 3/26/10	Thu 4/1/10	169					
171	Supplemental Remediation Sampling - Site Wide	109 days	Fri 2/19/10	Wed 7/21/10						
172	Scoping	5 days	Fri 2/19/10	Thu 2/25/10	138FS-5 days					
173	NDEP Meeting	1 day	Mon 2/22/10	Mon 2/22/10	172SS+1 day					
174	Work Plan	12 days	Fri 2/26/10	Mon 3/15/10						
175	Work Plan Draft	5 days	Fri 2/26/10	Thu 3/4/10	172					
176	Tronox/Chartis Review	5 days	Fri 3/5/10	Thu 3/11/10	175					
177	Submittal to NDEP	0 days	Thu 3/11/10	Thu 3/11/10	176					
178	NDEP Approval	2 days	Fri 3/12/10	Mon 3/15/10	177					
179	Bid Development	7 days	Fri 3/5/10	Mon 3/15/10						
180	SOW preparation	2 days	Fri 3/5/10	Mon 3/8/10	175					
181	Submittal to Contractors	0 days	Mon 3/8/10	Mon 3/8/10	180					
182	Contractor Selection	5 days	Tue 3/9/10	Mon 3/15/10	181					
183	Notice to Proceed	0 days	Mon 3/15/10	Mon 3/15/10	182					
184	Field Work	41 days	Tue 3/16/10	Tue 5/11/10	183					
185	Field Coordination/GBP	5 days	Tue 3/16/10	Mon 3/22/10	178,183FS-3 days					
186	Field Sampling	20 days	Tue 3/23/10	Mon 4/19/10	185					
187	Laboratory Analysis	39 days	Thu 3/18/10	Tue 5/11/10						
188	Mobile Laboratory Analysis	13 days	Thu 3/18/10	Mon 4/5/10						

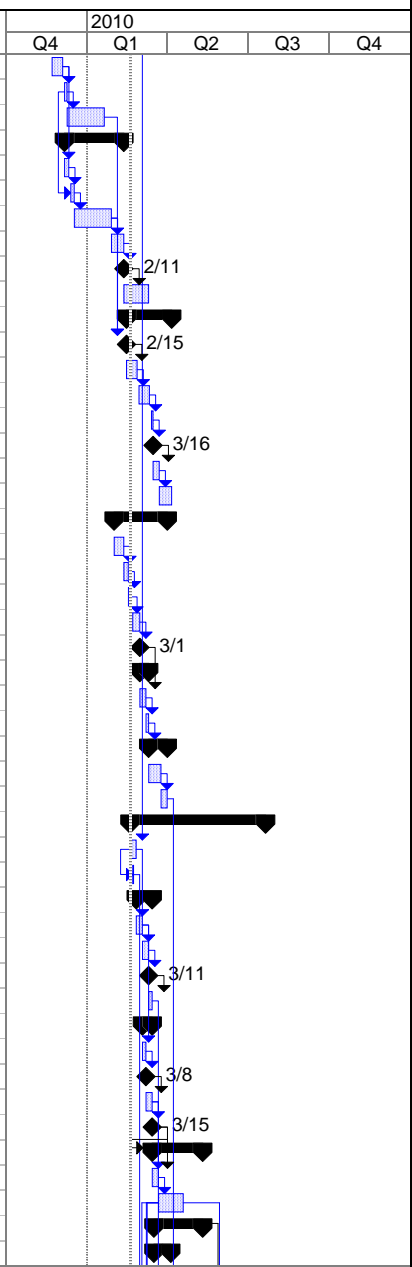


Task Progress Summary External Tasks Deadline Split Milestone Project Summary External Milestone

Tronox Phase B Remediation Program Schedule

February 18, 2010

For NDEP Review

ID	Task Name	Duration	Start	Finish	Predecessors	2010				
						Q4	Q1	Q2	Q3	Q4
189	Mobilization	3 days	Thu 3/18/10	Mon 3/22/10	182,186SS-3 days					
190	Analysis	10 days	Tue 3/23/10	Mon 4/5/10	189,186SS					
191	Fixed Lab Analysis	35 days	Wed 3/24/10	Tue 5/11/10	186SS+1 day					
192	Data Validation	20 days	Wed 5/12/10	Tue 6/8/10	191					
193	Data Validation Summary Report - Add'l Sampling	31 days	Wed 6/9/10	Wed 7/21/10						
194	Internal Draft DVSR	11 days	Wed 6/9/10	Wed 6/23/10	192					
195	Submit to NDEP	5 days	Thu 6/24/10	Wed 6/30/10	194					
196	NDEP Review	5 days	Thu 7/1/10	Wed 7/7/10	195					
197	Respond to Comments/DVSR Finalization	10 days	Thu 7/8/10	Wed 7/21/10	196					
198	NDEP Meeting	11 days	Wed 5/12/10	Wed 5/26/10						
199	Meeting Material Preparation	10 days	Wed 5/12/10	Tue 5/25/10	187					
200	Agency Meeting	1 day	Wed 5/26/10	Wed 5/26/10	199					
201	Removal Action Work Plan (Including PAMP, SWPPP)	137 days	Mon 2/1/10	Tue 8/10/10						
202	RAW Preparation	25 days	Mon 2/1/10	Fri 3/5/10						
203	Review RAW (Tronox, Chartis)	5 days	Mon 3/8/10	Fri 3/12/10	202					
204	Revise and Finalize RAW	5 days	Mon 3/15/10	Fri 3/19/10	202,203					
205	Submit RAW to NDEP	0 days	Fri 3/19/10	Fri 3/19/10	204					
206	NDEP Review	5 days	Mon 3/22/10	Fri 3/26/10	205					
207	Respond to Comments/RAW Finalization	10 days	Mon 3/29/10	Fri 4/9/10	206					
208	NDEP Approve RAW	5 days	Mon 4/12/10	Fri 4/16/10	207					
209	RAW Appendix- Area IV (to be supplanted by Preliminary Decision Units [PDU's])	21 days	Wed 5/12/10	Wed 6/9/10						
210	Appendix Preparation	10 days	Wed 5/12/10	Tue 5/25/10	191					
211	Review (Tronox, Chartis)	3 days	Wed 5/26/10	Fri 5/28/10	210					
212	Revise and Finalize RAW	3 days	Mon 5/31/10	Wed 6/2/10	210,211,186					
213	Submit RAW App to NDEP	0 days	Wed 6/2/10	Wed 6/2/10	212					
214	NDEP Review and Approve	5 days	Thu 6/3/10	Wed 6/9/10	213					
215	RAW Appendix- Area III (to be supplanted by PDU's)	25 days	Wed 6/9/10	Tue 7/13/10						
216	Appendix Preparation	10 days	Wed 6/9/10	Tue 6/22/10	192					
217	Review (Tronox, Chartis)	5 days	Wed 6/23/10	Tue 6/29/10	216					
218	Revise and Finalize RAW	5 days	Wed 6/30/10	Tue 7/6/10	217,216,192					
219	Submit to NDEP	0 days	Tue 7/6/10	Tue 7/6/10	218					
220	NDEP Review and Approve	5 days	Wed 7/7/10	Tue 7/13/10	219					
221	RAW Appendix - Area II (to be supplanted by PDU's)	35 days	Wed 6/16/10	Tue 8/3/10						
222	Appendix Preparation	10 days	Wed 6/16/10	Tue 6/29/10	192FS+5 days					
223	Review (Tronox, Chartis)	10 days	Wed 6/30/10	Tue 7/13/10	222					
224	Revise and Finalize	10 days	Wed 7/14/10	Tue 7/27/10	223,192					
225	Submit to NDEP	0 days	Tue 7/27/10	Tue 7/27/10	224					
226	NDEP Review and Approve	5 days	Wed 7/28/10	Tue 8/3/10	225					
227	RAW Appendix - Area I (to be supplanted by PDU's)	35 days	Wed 6/23/10	Tue 8/10/10						
228	Appendix Preparation	10 days	Wed 6/23/10	Tue 7/6/10	192FS+10 days					
229	Review (Tronox, Chartis)	10 days	Wed 7/7/10	Tue 7/20/10	228					
230	Revise and Finalize CAP	10 days	Wed 7/21/10	Tue 8/3/10	229					
231	Submit to NDEP	0 days	Tue 8/3/10	Tue 8/3/10	230					
232	NDEP Review and Approve	5 days	Wed 8/4/10	Tue 8/10/10	231					
233	Plans And Specifications/Contractor Selection	177 days	Mon 2/1/10	Tue 10/5/10						
234	Demolition	81 days	Mon 2/22/10	Mon 6/14/10						
235	Regulated Building Material Surveys	25 days	Mon 2/22/10	Fri 3/26/10						
236	Bid Specifications	5 days	Mon 2/22/10	Fri 2/26/10						

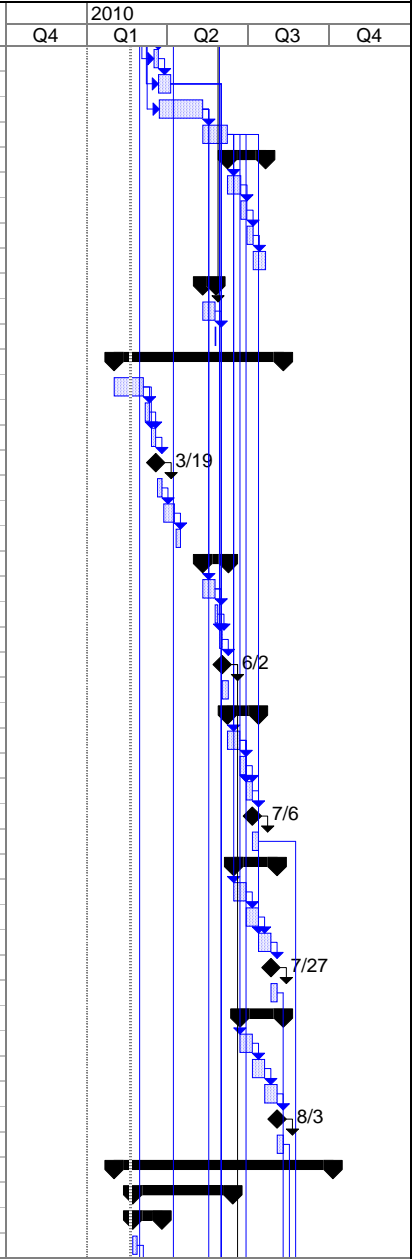

Task Progress Summary External Tasks Deadline


Split Milestone Project Summary External Milestone

Tronox Phase B Remediation Program Schedule

February 18, 2010

For NDEP Review

ID	Task Name	Duration	Start	Finish	Predecessors	2010				
						Q4	Q1	Q2	Q3	Q4
237	Submit Bid Specs	0 days	Fri 2/26/10	Fri 2/26/10	236		●			
238	Receive Bids	5 days	Mon 3/1/10	Fri 3/5/10	237					
239	Select Contractor	5 days	Mon 3/8/10	Fri 3/12/10	238					
240	Conduct Surveys	10 days	Mon 3/15/10	Fri 3/26/10	239					
241	Prepare Demo and Abatement Plans and Specifications	35 days	Mon 3/29/10	Fri 5/14/10	240					
242	Review Plans and Specifications (Tronox, Chartis)	5 days	Mon 5/17/10	Fri 5/21/10	241					
243	Issue Plans and Specifications	5 days	Mon 5/24/10	Fri 5/28/10	242					
244	Bid Walk	1 day	Mon 5/31/10	Mon 5/31/10	243					
245	Bid Submittal Date	5 days	Tue 6/1/10	Mon 6/7/10	244					
246	Review Bids and Award Contract	5 days	Tue 6/8/10	Mon 6/14/10	245					
247	Remediation	177 days	Mon 2/1/10	Tue 10/5/10						
248	Mn Tailings	28 days	Fri 2/12/10	Tue 3/23/10						
249	Prepare Remediation Plans and Specifications	10 days	Fri 2/12/10	Thu 2/25/10						
250	Review Plans and Specifications (Tronox, Chartis)	5 days	Fri 2/26/10	Thu 3/4/10	249					
251	Issue Plans and Specifications	3 days	Fri 3/5/10	Tue 3/9/10	250					
252	Bid Submittal Date	5 days	Wed 3/10/10	Tue 3/16/10	251					
253	Review Bids, Contract Negotiation and Award	5 days	Wed 3/17/10	Tue 3/23/10	252					
254	Site Wide - less specific detail for remediation areas	51 days	Mon 2/1/10	Mon 4/12/10						
255	Prepare Remediation Plans and Specifications	30 days	Mon 2/1/10	Fri 3/12/10						
256	Review Plans and Specifications (Tronox, Chartis)	5 days	Mon 3/15/10	Fri 3/19/10	255					
257	Issue Plans and Specifications	5 days	Mon 3/22/10	Fri 3/26/10	256					
258	Bid Walk	1 day	Mon 3/29/10	Mon 3/29/10	257					
259	Bid Submittal Date	5 days	Tue 3/30/10	Mon 4/5/10	258					
260	Review Bids, Contract Negotiation and Award	5 days	Tue 4/6/10	Mon 4/12/10	259					
261	Area IV	20 days	Thu 6/3/10	Wed 6/30/10						
262	Prepare Remediation Plans and Specifications	10 days	Thu 6/3/10	Wed 6/16/10	213					
263	Review Plans and Specifications (Tronox, Chartis)	5 days	Thu 6/17/10	Wed 6/23/10	262					
264	Issue Plans and Specifications	5 days	Thu 6/24/10	Wed 6/30/10	263					
265	Area III	20 days	Wed 6/23/10	Tue 7/20/10						
266	Prepare Remediation Plans and Specifications	10 days	Wed 6/23/10	Tue 7/6/10	216					
267	Review Plans and Specifications (Tronox, Chartis)	5 days	Wed 7/7/10	Tue 7/13/10	266					
268	Issue Plans and Specifications	5 days	Wed 7/14/10	Tue 7/20/10	267					
269	Area II	20 days	Wed 8/4/10	Tue 8/31/10						
270	Prepare Remediation Plans and Specifications	10 days	Wed 8/4/10	Tue 8/17/10	226					
271	Review Plans and Specifications (Tronox, Chartis)	5 days	Wed 8/18/10	Tue 8/24/10	270					
272	Issue Plans and Specifications	5 days	Wed 8/25/10	Tue 8/31/10	271,220					
273	Area I	40 days	Wed 8/11/10	Tue 10/5/10						
274	Prepare Remediation Plans and Specifications	30 days	Wed 8/11/10	Tue 9/21/10	232					
275	Review Plans and Specifications (Tronox, Chartis)	5 days	Wed 9/22/10	Tue 9/28/10	274					
276	Issue Plans and Specifications	5 days	Wed 9/29/10	Tue 10/5/10	275					
277	Grading and Dust Monitoring Permit	56 days	Mon 2/22/10	Mon 5/10/10						
278	Parcels C, D, F, G, and H	15 days	Mon 2/22/10	Fri 3/12/10						
279	Permits - Mn Tailings	15 days	Mon 3/8/10	Fri 3/26/10						
280	Permits - Other Areas	15 days	Mon 4/12/10	Fri 4/30/10	257FS+10 days					
281	Contractor Submits Grading and DMP	5 days	Tue 4/13/10	Mon 4/19/10	260					
282	Clark County Review/Permitting	15 days	Tue 4/20/10	Mon 5/10/10	281					
283	Demolition	53 days	Tue 6/15/10	Thu 8/26/10						
284	Mobilization	3 days	Tue 6/15/10	Thu 6/17/10	246					

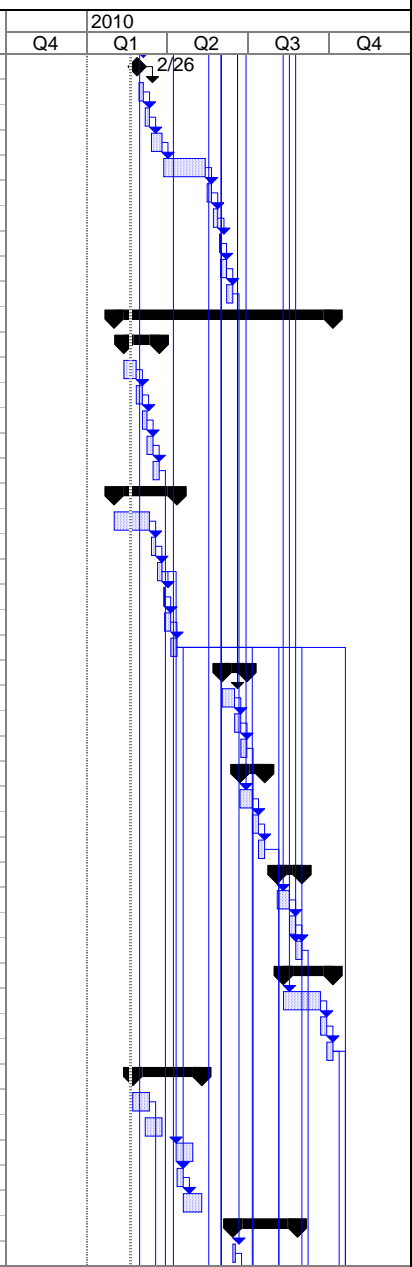

Task Progress Summary External Tasks Deadline


Split Milestone Project Summary External Milestone

Tronox Phase B Remediation Program Schedule

February 18, 2010

For NDEP Review

ID	Task Name	Duration	Start	Finish	Predecessors	2010				
						Q4	Q1	Q2	Q3	Q4
285	Demolish Applicable Bldgs	20 days	Fri 6/18/10	Thu 7/15/10	284					
286	Remove Applicable Utilities	30 days	Fri 7/2/10	Thu 8/12/10	285FS-10 days					
287	Install Temporary Critical Utilities	10 days	Fri 8/13/10	Thu 8/26/10	286					
288	Soil Remediation	435 days	Wed 4/15/09	Tue 12/14/10						
289	Identify Backfill Source(s)	70 days	Mon 3/1/10	Fri 6/4/10						
290	Identify Potential Sources	20 days	Mon 3/1/10	Fri 3/26/10						
291	"Phase I" Evaluations	40 days	Mon 3/15/10	Fri 5/7/10	290FS-10 days					
292	Soil Certification	20 days	Mon 5/10/10	Fri 6/4/10	291					
293	Soil Sampling and Analysis	20 days	Mon 5/10/10	Fri 6/4/10						
294	Implementation of SWPPP Measures	45 days	Wed 4/15/09	Tue 6/16/09						
295	Parcels C, D, F, G and H	40 days	Mon 2/15/10	Fri 4/9/10						
296	Contractor Selection	20 days	Mon 2/15/10	Fri 3/12/10						
297	Notice to Proceed	0 days	Fri 3/12/10	Fri 3/12/10	296					
298	Excavate, Transport to TSDF	10 days	Mon 3/15/10	Fri 3/26/10	297,278					
299	Collect and Evaluate Confirmation Samples	20 days	Mon 3/15/10	Fri 4/9/10	298FS-10 days					
300	Contractor Mobilization	5 days	Wed 3/24/10	Tue 3/30/10	253					
301	Mn Tailings	70 days	Wed 3/31/10	Tue 7/6/10						
302	Excavate, Transport to TSDF	14 wks	Wed 3/31/10	Tue 7/6/10	300					
303	Area IV	15 days	Wed 7/7/10	Tue 7/27/10						
304	Excavate, Transport to TSDF	15 days	Wed 7/7/10	Tue 7/27/10	264,302,285FS-15 d					
305	Area III	15 days	Fri 8/6/10	Thu 8/26/10						
306	Excavate, Transport to TSDF	15 days	Fri 8/6/10	Thu 8/26/10	268,304,285FS-5 d					
307	Area II	43 days	Fri 8/20/10	Tue 10/19/10						
308	Haul Road Development	5 days	Fri 8/20/10	Thu 8/26/10	306FS-5 days					
309	Excavate, Transport to TSDF	35 days	Wed 9/1/10	Tue 10/19/10	272,285,286,260,30					
310	Area I	40 days	Wed 10/13/10	Tue 12/7/10						
311	Haul Road Development	5 days	Wed 10/13/10	Tue 10/19/10	309FS-5 days					
312	Excavate, Transport to TSDF	35 days	Wed 10/20/10	Tue 12/7/10	276,285,286,260,31					
313	Contractor Demobilization	5 days	Wed 12/8/10	Tue 12/14/10	312					
314	Data Validation and DVSR Reports	35 days	Mon 4/12/10	Fri 5/28/10						
315	Data Validation Summary Report - Parcels C, D, F, G and H	35 days	Mon 4/12/10	Fri 5/28/10						
316	Internal Draft DVSR	15 days	Mon 4/12/10	Fri 4/30/10	299					
317	Client Review/Draft Finalization	5 days	Mon 5/3/10	Fri 5/7/10	316					
318	Submit to NDEP	0 days	Fri 5/7/10	Fri 5/7/10	317					
319	NDEP Review	5 days	Mon 5/10/10	Fri 5/14/10	318					
320	Respond to Comments/DVSR Finalization	10 days	Mon 5/17/10	Fri 5/28/10	319					
321	Replace Utility Lines as Necessary	105 days	Wed 7/28/10	Tue 12/21/10						
322	Area IV	20 days	Wed 7/28/10	Tue 8/24/10	304					
323	Area III	20 days	Fri 8/27/10	Thu 9/23/10	306					
324	Area II	20 days	Wed 10/20/10	Tue 11/16/10	309					
325	Area I	10 days	Wed 12/8/10	Tue 12/21/10	312					
326	Environmental Covenants	127 days	Mon 7/5/10	Tue 12/28/10						
327	Develop EC Plan	60 days	Mon 7/5/10	Fri 9/24/10						
328	Develop Risk Management Plan	60 days	Mon 7/12/10	Fri 10/1/10						
329	Cap Pond Berms	30 days	Wed 10/6/10	Tue 11/16/10	276					
330	Cap Remaining Impacted Soils -if necessary	90 days	Wed 8/25/10	Tue 12/28/10						
331	Area IV	20 days	Wed 8/25/10	Tue 9/21/10	322					
332	Area III	20 days	Fri 9/24/10	Thu 10/21/10	323					




Tronox Phase B Remediation Program Schedule

February 18, 2010

For NDEP Review

ID	Task Name	Duration	Start	Finish	Predecessors	2010				
						Q4	Q1	Q2	Q3	Q4
333	Area II	10 days	Wed 11/17/10	Tue 11/30/10	324					
334	Area I	5 days	Wed 12/22/10	Tue 12/28/10	325					
335	Backfill of Excavations, if required/Finish Grading	80 days	Wed 9/22/10	Tue 1/11/11						
336	Area IV	20 days	Wed 9/22/10	Tue 10/19/10	331					
337	Area III	20 days	Fri 10/22/10	Thu 11/18/10	332					
338	Area II	10 days	Wed 12/1/10	Tue 12/14/10	333					
339	Area I	10 days	Wed 12/29/10	Tue 1/11/11	334					
340	Construction Management/Oversight	206 days	Tue 3/30/10	Tue 1/11/11	297,339FF					
341	Perchlorate Soil Flushing Pilot Test	112 days	Mon 3/1/10	Tue 8/3/10						
342	Pilot Test Workplan	52 days	Mon 3/1/10	Tue 5/11/10						
343	Workplan Preparation	10 days	Mon 3/1/10	Fri 3/12/10						
344	Review Workplan (Tronox, Chartis)	5 days	Mon 3/15/10	Fri 3/19/10	343					
345	Revise and Finalize WP	5 days	Mon 3/22/10	Fri 3/26/10	344					
346	Submit WP to NDEP	0 days	Fri 3/26/10	Fri 3/26/10	345					
347	NDEP Review	5 days	Mon 3/29/10	Fri 4/2/10	346					
348	Respond to Comments/WP Finalization	10 days	Mon 4/5/10	Fri 4/16/10	347					
349	NDEP Approval	2 days	Mon 4/19/10	Tue 4/20/10	348					
350	Column Test	15 days	Tue 4/20/10	Tue 5/11/10	349					
351	Contractor Selection	10 days	Wed 4/21/10	Tue 5/4/10	343					
352	Notice to Proceed	0 days	Tue 4/20/10	Tue 4/20/10	349					
353	Implementation	15 days	Wed 4/21/10	Tue 5/11/10						
354	Pilot Test Implementation	12 wks	Wed 5/12/10	Tue 8/3/10	347,350					
355	Full Scale Implementation	51 days	Wed 8/4/10	Wed 10/13/10						
356	Prepare Remediation Plans and Specifications	10 days	Wed 8/4/10	Tue 8/17/10	354					
357	Review Plans and Specifications (Tronox, Chartis)	5 days	Wed 8/18/10	Tue 8/24/10	356					
358	Issue Plans and Specifications	5 days	Wed 8/25/10	Tue 8/31/10	357					
359	Bid Walk	1 day	Wed 9/1/10	Wed 9/1/10	358					
360	Bid Submittal Date	5 days	Thu 9/2/10	Wed 9/8/10	359					
361	Review Bids and Award Contract	5 days	Thu 9/9/10	Wed 9/15/10	360					
362	Installation	20 days	Thu 9/16/10	Wed 10/13/10	361					
363	Human Health Risk Evaluation	162 days	Mon 1/4/10	Tue 8/17/10						
364	Human Health Risk WP	48 days	Mon 1/4/10	Wed 3/10/10						
365	HHRA WP Revisions	23 days	Mon 1/4/10	Wed 2/3/10						
366	HHRA WP Finalization	25 days	Thu 2/4/10	Wed 3/10/10	365					
367	NDEP Review and Approve	0 days	Wed 3/10/10	Wed 3/10/10	366					
368	Probabilistic HHRA (PRA) WP	55 days	Thu 3/25/10	Wed 6/9/10						
369	PRA Development	20 days	Thu 3/25/10	Wed 4/21/10	367FS+10 days					
370	Review PRA and (Tronox, Chartis)	10 days	Thu 4/22/10	Wed 5/5/10	369					
371	Revise and Finalize PRA	10 days	Thu 5/6/10	Wed 5/19/10	370					
372	Submit PRA to NDEP	0 days	Wed 5/19/10	Wed 5/19/10	371					
373	NDEP Review and Approve	15 days	Thu 5/20/10	Wed 6/9/10	372					
374	Human Health Risk Evaluation/Reports	126 days	Tue 2/23/10	Tue 8/17/10						
375	Decision Unit Development	71 days	Tue 2/23/10	Tue 6/1/10						
376	Preliminary Decision Unit (PDU) Development	5 days	Tue 2/23/10	Mon 3/1/10	173					
377	CSM Refinement	10 days	Tue 3/2/10	Mon 3/15/10	376					
378	Decision Unit Determination	15 days	Wed 5/12/10	Tue 6/1/10	191,377FS-10 days					
379	Evaluation of Site-Specific Risk Based Goals	20 days	Fri 4/2/10	Thu 4/29/10	170					
380	Post Closure Risk Assessment	55 days	Wed 6/2/10	Tue 8/17/10						

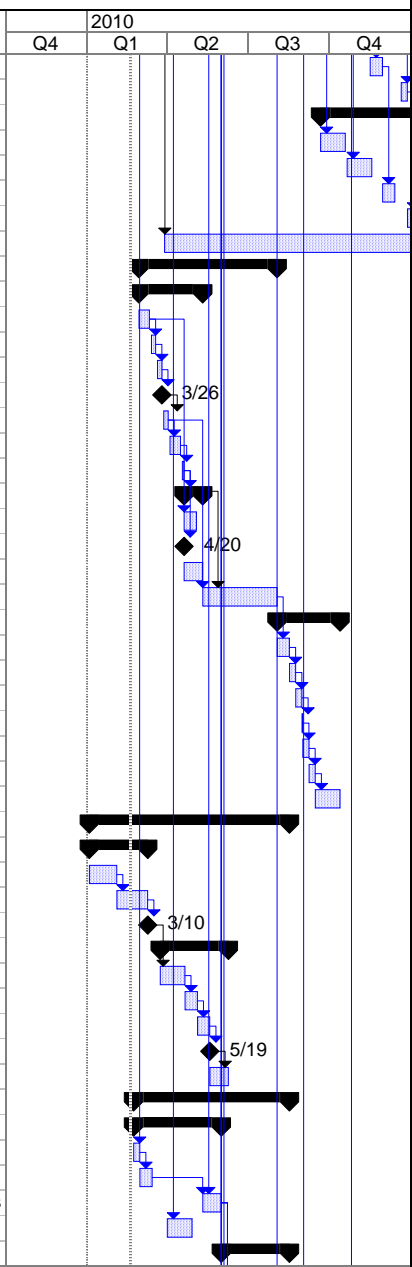

Task Progress Summary External Tasks Deadline


 Split Milestone Project Summary External Milestone

Tronox Phase B Remediation Program Schedule

February 18, 2010

For NDEP Review

ID	Task Name	Duration	Start	Finish	Predecessors	2010				
						Q4	Q1	Q2	Q3	Q4
381	Area IV - will actually be based on DU's once developed	45 days	Wed 6/2/10	Tue 8/3/10						
382	Prepare HHRA	20 days	Wed 6/2/10	Tue 6/29/10	190,378					
383	Review RA (Tronox, Chartis)	10 days	Wed 6/30/10	Tue 7/13/10	382					
384	Revise and Finalize	10 days	Wed 7/14/10	Tue 7/27/10	383					
385	Submit RA to NDEP	0 days	Tue 7/27/10	Tue 7/27/10	384					
386	NDEP Review and Approve RA	5 days	Wed 7/28/10	Tue 8/3/10	385					
387	Area II - will actually be based on DU's once developed	55 days	Wed 6/2/10	Tue 8/17/10						
388	Prepare HHRA	20 days	Wed 6/2/10	Tue 6/29/10	190,378					
389	Review RA (Tronox, Chartis)	10 days	Wed 6/30/10	Tue 7/13/10	388					
390	Revise and Finalize	10 days	Wed 7/14/10	Tue 7/27/10	389					
391	Submit RA to NDEP	0 days	Tue 7/27/10	Tue 7/27/10	390					
392	NDEP Review and Approve RA	15 days	Wed 7/28/10	Tue 8/17/10	391					
393	Area I - will actually be based on DU's once developed	55 days	Wed 6/2/10	Tue 8/17/10						
394	Prepare HHRA	20 days	Wed 6/2/10	Tue 6/29/10	190,378					
395	Review RA (Tronox, Chartis)	10 days	Wed 6/30/10	Tue 7/13/10	394					
396	Revise and Finalize	10 days	Wed 7/14/10	Tue 7/27/10	395					
397	Submit RA to NDEP	0 days	Tue 7/27/10	Tue 7/27/10	396					
398	NDEP Review and Approve RA	15 days	Wed 7/28/10	Tue 8/17/10	397					
399	Soil Vapor Intrusion Evaluation and Mitigation	180 days	Mon 1/4/10	Fri 9/10/10						
400	Evaluate Soil Gas Data	10 days	Mon 1/4/10	Fri 1/15/10						
401	Evaluate Phase B Soil Data	10 days	Mon 1/18/10	Fri 1/29/10	400					
402	Evaluate Need for Mitigation	45 days	Mon 3/1/10	Fri 4/30/10						
403	IAQ Testing (if required)	45 days	Mon 3/1/10	Fri 4/30/10						
404	Contractor Selection	15 days	Mon 3/1/10	Fri 3/19/10	401FS+20 days					
405	Implementation	15 days	Mon 3/22/10	Fri 4/9/10	404					
406	Data Evaluation	15 days	Mon 4/12/10	Fri 4/30/10	405					
407	Mitigation (if required)	95 days	Mon 5/3/10	Fri 9/10/10	406					
408	Pilot Test Design	10 days	Mon 5/3/10	Fri 5/14/10						
409	Pilot Test Workplan/Approval	25 days	Mon 5/17/10	Fri 6/18/10	408					
410	Pilot Test	10 days	Mon 6/21/10	Fri 7/2/10	400FS+30 days,409					
411	System design	15 days	Mon 7/5/10	Fri 7/23/10	410					
412	Install Sub Slab Depressurization or retrofit existing building(s), if required	30 days	Mon 7/26/10	Fri 9/3/10	411					
413	System Start Up	5 days	Mon 9/6/10	Fri 9/10/10	412					
414	Operations and Maintenance (not scheduled)	0 days	Fri 9/10/10	Fri 9/10/10	413					
415	Soil Vapor Evaluation Report	177 days	Mon 5/3/10	Tue 1/4/11	406					
416	Prepare Report	20 days	Mon 5/3/10	Fri 5/28/10	406					
417	Review (Tronox, Chartis)	10 days	Mon 5/31/10	Fri 6/11/10	416					
418	Revise and Finalize	10 days	Mon 6/14/10	Fri 6/25/10	417					
419	Submit to NDEP	0 days	Fri 6/25/10	Fri 6/25/10	418					
420	NDEP Review and Approve	5 days	Mon 6/28/10	Fri 7/2/10	419					
421	Closures	157 days	Mon 5/31/10	Tue 1/4/11						
422	Parcel C, D, F, G and H	55 days	Mon 5/31/10	Fri 8/13/10						
423	Prepare Closure Report	20 days	Mon 5/31/10	Fri 6/25/10	320					
424	Review CR (Tronox, Chartis)	10 days	Mon 6/28/10	Fri 7/9/10	423					
425	Revise and Finalize CR	10 days	Mon 7/12/10	Fri 7/23/10	424					
426	Submit CR to NDEP	0 days	Fri 7/23/10	Fri 7/23/10	425					
427	NDEP Review and Approve CR	15 days	Mon 7/26/10	Fri 8/13/10	426					
428	Area IV - will actually be based on decision units once developed	55 days	Wed 7/28/10	Tue 10/12/10						

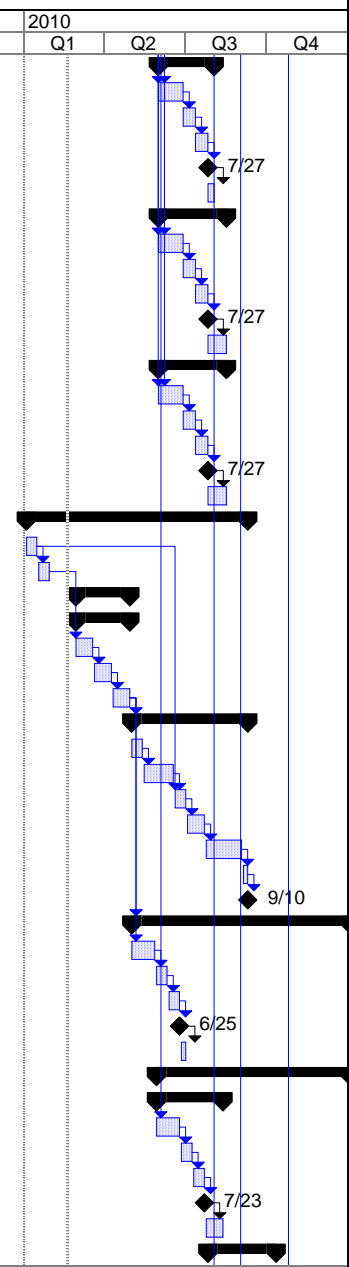

Task Progress Summary External Tasks Deadline


 Split Milestone Project Summary External Milestone

Tronox Phase B Remediation Program Schedule

February 18, 2010

For NDEP Review

ID	Task Name	Duration	Start	Finish	Predecessors	2010				
						Q4	Q1	Q2	Q3	Q4
429	Prepare Closure Report	20 days	Wed 7/28/10	Tue 8/24/10	304					
430	Review CR (Tronox, Chartis)	10 days	Wed 8/25/10	Tue 9/7/10	429					
431	Revise and Finalize CR	10 days	Wed 9/8/10	Tue 9/21/10	430					
432	Submit CR to NDEP	0 days	Tue 9/21/10	Tue 9/21/10	431					
433	NDEP Review and Approve CR	15 days	Wed 9/22/10	Tue 10/12/10	432					
434	Area II - will actually be based on decision units once developed	55 days	Fri 8/27/10	Thu 11/11/10						
435	Prepare Closure Report	20 days	Fri 8/27/10	Thu 9/23/10	306					
436	Review CR (Tronox, Chartis)	10 days	Fri 9/24/10	Thu 10/7/10	435					
437	Revise and Finalize CR	10 days	Fri 10/8/10	Thu 10/21/10	436					
438	Submit CR to NDEP	0 days	Thu 10/21/10	Thu 10/21/10	437					
439	NDEP Review and Approve CR	15 days	Fri 10/22/10	Thu 11/11/10	438					
440	Area I - will actually be based on decision units once developed	55 days	Wed 10/20/10	Tue 1/4/11						
441	Prepare Closure Report	20 days	Wed 10/20/10	Tue 11/16/10	309					
442	Review CR (Tronox, Chartis)	10 days	Wed 11/17/10	Tue 11/30/10	441					
443	Revise and Finalize CR	10 days	Wed 12/1/10	Tue 12/14/10	442					
444	Submit CR to NDEP	0 days	Tue 12/14/10	Tue 12/14/10	443					
445	NDEP Review and Approve CR	15 days	Wed 12/15/10	Tue 1/4/11	444					

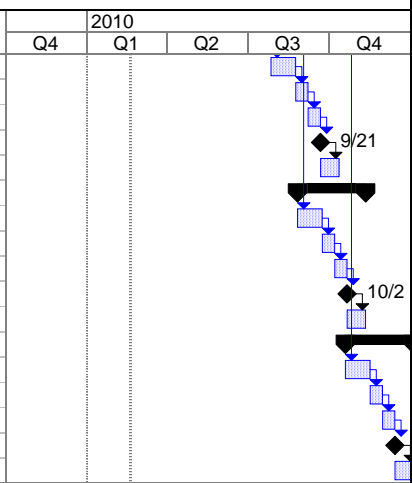

Task Progress Summary External Tasks Deadline Split Milestone Project Summary External Milestone
